

**BIDS AND AWARDS COMMITTEE (BAC) FOR GOODS**

**BIDDING OF FIT-OUT AND REPAIR FOR THE SUBIC-CLARK RAILWAY PROJECT  
MANAGEMENT OFFICE VIA NEGOTIATED PROCUREMENT**

**RESOLUTION NO. BG-FR-2021-001**

**WHEREAS**, the **BASES CONVERSION AND DEVELOPMENT AUTHORITY (BCDA)** has approved the **Bidding of Fit-out and Repair for the Subic-Clark Railway Project Management Office via Negotiated Procurement** with the Approved Budget for the Contract (ABC) in the amount of Php2,850,000.00, inclusive of all applicable government taxes and fees, through the General Appropriations Act (GAA);

**WHEREAS**, the Bids and Awards Committee for Goods (**BAC-G**), through its Secretariat, advertised the Invitation to Bid on 14 October 2021 in the following:

- DBM Philippine Government Electronic Procurement System (PhilGEPS);
- BCDA Website; and
- In a conspicuous place reserved for the purpose in the premises of BCDA.

**WHEREAS**, in response to the said advertisements, the following companies have responded, brought bidding documents, and submitted bid proposals before the deadline for submission of bids on 29 October 2021 at 12:00 PM:

- DCLABR03 Construction;
- Kalahan General Construction and Supplies;
- Jaymar Builders; and
- FPF Construction

**WHEREAS**, during the Opening of Bids on 29 October 2021, the BAC-G opened the bidding documents of the above-mentioned bidders and noted the following:

- Both DCLABR03 Construction and Jaymar Builders were declared eligible after the preliminary evaluation; and
- Both Kalahan General Construction and Supplies and FPF Construction have failed to submit complete eligibility and technical documents, therefore, they were declared non-eligible, as shown in the table below. Pursuant to Section 25.2. (a) vii of the RIRR of RA 9184, their financial proposals were left unopened:

<b>Eligibility and Technical Requirements</b>	<b>KALAHAN GENERAL CONSTRUCTION AND SUPPLIES</b>	<b>FPF CONSTRUCTION</b>
<b>Conformity with the Technical Specifications Compliance Form</b> (Use the supplied Technical Specifications	<b>(Failed)</b> <b>Technical Specifications compliance Section has no</b>	Passed

Compliance Form found in the Bid Documents as Section VII)	<b>remarks</b>	
<b>Notarized Omnibus Sworn Statement</b> , in accordance with Section 25.3 of the 2016 Revised IRR of RA 9184, and using the form prescribed in Section VIII. Bidding Forms  Note: The Omnibus Sworn Statement shall be accompanied by the duly notarized Special Power of Attorney, Board/Partnership Resolution, or Secretary's Certificate, whichever is applicable	Passed	<b>(Failed)</b> <b>No Submission of SPA/Partnership Resolution, or Secretary's Certificate</b>
<b>Latest Audited Financial Statements</b> , showing, among others, the Supplier's total and current assets and liabilities, stamped "received" by the BIR or it's duly accredited and authorized institutions, for the preceding calendar year which should not be earlier than two (2) years from the date of submission of bid	Passed	<b>(Failed)</b> <b>Non Submission of Latest Audited Financial Statements</b>
<b>REMARKS</b>	<b>Not Eligible / Failed</b>	<b>Not Eligible / Failed</b>

**WHEREAS**, BAC-G opened both the financial proposals of DCLABR03 Construction and Jaymar Builders, both being eligible, and observed the following:

<b>Name of Bidder</b>	<b>Financial Bid</b>
DCLABR03 Construction	Php2,622,000.00
Jaymar Builders	Php2,800,000.00

*The Abstract of Bids is hereby attached as **Annex A**.*

**WHEREAS**, During the Technical Working Group's (TWG) detailed evaluation from 29 October to 03 November 2021, pursuant to Section 32 of Rule IX of the Revised IRR of RA 9184, the TWG noted a variance of P21,983.10 as follows:

<b>Particulars</b>	<b>Financial Proposal</b>
As submitted	Php2,622,000.00
As computed by the TWG	Php2,600,016.90
Variance	PhP21,983.10

**WHEREAS**, The submission of DCLABRO3 for item no. 5.5 (Glass partitions) is in sq.m and not in sq.ft as stated in the Terms of Reference;

**WHEREAS**, Upon conversion of the unit for the Glass partitions, per the requirement in the TOR, DCLABRO3's computation was overstated by P21,983.10 as shown in the table thereunder:

Particulars	Description in Unit	Unit Cost	Total Amount
As per TOR	<b>121.11 SQ.FT.</b>		
As submitted by DCLabro3	18.75 SQ.M.	2,931.08	54,957.75
As computed by the TWG with conversion from SQ.FT. to SQ.M.	11.25 SQ.M.	2,931.08	32,974.65
<b>VARIANCE (Php)</b>			<b>21,983.10</b>

**WHEREAS**, pursuant to to Section 32.2.3(c) of the 2016 Revised IRR of RA 9184, in case of discrepancies, the actual sum of prices of component items shall prevail over the stated total price, thus the BAC-G considers the **Php 2,600,016.90** as the correct and final bid amount.

**WHEREAS**, DCLABRO3 Construction was declared as the Bidder with the Lowest Calculated Bid (LCB) with financial proposal amounting to **Two Million Six Hundred Thousand Sixteen Pesos and 90/100 Only (Php 2,600,016.90)**, inclusive of VAT and all applicable taxes and fees, and was qualified for the post-qualification.

**WHEREAS**, BAC-G informed DCLABRO3 Construction in its letter of Post Qualification Notice dated 03 November 2021 that DCLABRO3 Construction's financial bid was in fact, the amount of **Two Million Six Hundred Thousand Sixteen Pesos and 90/100 Only (Php 2,600,016.90)**, inclusive of all applicable taxes and fees;

**WHEREAS**, pursuant to Rule X of the RIRR of RA 9184, the Technical Working Group (TWG) of BAC-G conducted a post qualification with DCLABRO3 Construction on 05-08 November 2021 to determine whether it complies with and is responsive to the requirements and conditions specified in the Bidding Documents for the **Bidding of Fit-out and Repair for the Subic-Clark Railway Project Management Office via Negotiated Procurement**;

**WHEREAS**, after the careful examination, validation, and verification of all the eligibility, technical, and financial documents submitted to the BAC-G by the DCLABRO3 Construction, its bid was declared Complying and Responsive (*Post Qualification Report attached as Annex B*).

**NOW, THEREFORE**, we, the Members of the Bids and Awards Committee for Goods, hereby **RESOLVE** as it is hereby **RESOLVED** to recommend the following:


- a. To declare DCLABRO3 Construction as the Bidder with the Lowest Calculated and Responsive Bid (LCRB) for the Bidding of Fit-out and Repair for the Subic-Clark Railway Project Management Office via Negotiated Procurement;
- b. To award the Contract to DCLABRO3 Construction in the amount of **Two Million Six Hundred Thousand Sixteen Pesos and 90/100 Only (Php 2,600,016.90)**, inclusive of all applicable taxes and fees;

- c. To issue the corresponding Notice of Award to DCLABR03 Construction (Copy Attached); and
- d. To direct the Subic Clark Railway Project (SCRP) PMO, being the end-user unit, to furnish the BAC-G copies of the duly conformed Notice of Award, Notice to Proceed and the duly executed agreement/contract.

**RESOLVED**, at the BCDA Corporate Center Office, Bonifacio Global City, Taguig City, this 12 November 2021.

**BIDS AND AWARDS COMMITTEE (BAC) FOR GOODS**

  
**JOSHUA M. BINGCANG**  
Chairperson

  
**JOCELYN L. CANIONES**  
Vice Chairperson

  
**SAMUEL JOHN VIDALLON**  
Member

  
**CHRISTIAN T. DULDULAO**  
Member

  
**RITCHIE P. PACLIBAR**  
Member

Approved By:

  
**AILEEN ANUNCIACION R. ZOSA**  
Executive Vice President

BACG2021-0181

12 November 2021

**DONALDITO P. GASPAY**

Authorized Representative  
DCLABRO3 Construction  
City of Borongan  
Province of Eastern Samar

Subject: **NOTICE OF AWARD**  
Bidding of Fit-out and Repair for the Subic–Clark Railway Project  
Management Office via Negotiated Procurement

Dear **Mr. Gaspay**:

The Bases Conversion and Development Authority (BCDA) hereby awards the contract to **DCLABRO3 CONSTRUCTION** for having submitted the Lowest Calculated and Responsive Bid (LCRB) for the **Bidding of Fit-out and Repair for the Subic–Clark Railway Project Management Office via Negotiated Procurement** with the amount of **Two Million Six Hundred Thousand Sixteen Pesos and 90/100 Only (Php 2,600,016.90)**, inclusive of all applicable taxes and fees

You are therefore required, within ten (10) calendar days from the receipt of this Notice of Award, to:

1. Formally enter into contract with BCDA and comply with all the documentary requirements; and
2. Post a Performance Security denominated in Philippine Pesos in any of the form and in the amount stipulated in Section 39.2 of the revised IRR of RA 9184 which shall be posted in favor of BCDA and which shall remain valid until the issuance of Certificate of Final Acceptance, as follows:

FORM OF PERFORMANCE SECURITY	AMOUNT OF PERFORMANCE SECURITY (Equal to % of the Total Contract Price)
a. Cash or cashier's/manager's check issued by a Universal or Commercial Bank.	Five percent (5%)
b. Bank draft/guarantee or irrevocable letter of credit issued by a Universal or Commercial Bank: Provided, however, that it shall be confirmed or authenticated by a Universal or	

Commercial Bank, if issued by a foreign bank.	
c. Surety bond callable upon demand issued by a surety or insurance company duly certified by the Insurance Commission as authorized to issue such security; and/or	Thirty percent (30%)

Failure to enter into said contract and/or provide the Performance Security shall constitute sufficient ground for cancellation of the award.

Thank you.

Very truly yours,



**AILEEN AN. R. ZOSA**  
Executive Vice President

Date: \_\_\_\_\_

Conforme:

**DONALDITO P. GASPAY**  
Authorized Representative

Date: \_\_\_\_\_

BACG2021-0182

# **Annex A**

## BASES CONVERSION AND DEVELOPMENT AUTHORITY

### NEGOTIATED PROCUREMENT FOR THE FIT-OUT AND REPAIR FOR SUBIC-CLARK RAILWAY PROJECT MANAGEMENT OFFICE

29 October 2021 / 2:00 PM / BCDA CONFERENCE A & B

#### ABSTRACT OF BIDS AS READ (ELIGIBILITY AND FINANCIAL DOCUMENTS)

Name of Bidders		DCLABRO3 CONSTRUCTION	KALAHAN GENERAL CONSTRUCTION AND SUPPLIES	JAYMAR BUILDERS	FPF CONSTRUCTION
Date & Time Submitted (Deadline 29 October 2021 @12:00 NN)		29 October 2021 @ 8:34 AM	29 October 2021 @ 8:45 AM	29 October 2021 @9:50AM	29 October 2021 @11:36AM
<b>ELIGIBILITY AND FINANCIAL DOCUMENTS</b>					
	<b>Original</b>	<b>Submitted</b>	<b>Submitted</b>	<b>Submitted</b>	<b>Submitted</b>
<b>CHECKLIST OF REQUIREMENTS</b>					
<b>TAB A</b>	PhilGEPS Certificate of Registration <b>under Platinum</b> Membership (all pages)  <i>In case the bidder opted to submit their Class "A" Documents, the Certificate of PhilGEPS Registration (Platinum</i>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>

Abstract of Bid as Read re: Negotiated Procurement for the Fit-out And Repair of the Subic-Clark Railway Project Management Office



	<i>Membership) shall remain as a post-qualification requirement to be submitted in accordance with Section 34.2 of the 2016 Revised IRR of RA 9184</i>				
<b>TAB B</b>	<p>(FORM SF-G&amp;S-19A) <b>Statement of all its ongoing government and private contracts</b>, including contracts awarded but not yet started, if any, whether similar or not similar in nature and complexity to the contract to be bid;</p> <p>(FORM SF-G&amp;S-19B) <b>Statement of Single Largest Completed Contract (SLCC)</b>. Statement of One (1) COMPLETED government and/or private contract similar in nature to the contract to be bid equivalent to at least fifty percent (50%) of the ABC completed within 5 years prior to the deadline for the submission and receipt of bids (<i>Section IX, Bidding Forms</i>)</p> <p>The Statement of SLCC to be submitted by the bidder shall attach ANY of the following proof:</p> <ul style="list-style-type: none"> <li>❖ end user's acceptance; or</li> <li>❖ official receipt of the last payment received; or</li> <li>❖ sales invoice</li> </ul>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>
<b>TAB</b>	<b><u>Bid Security in ANY of the following:</u></b>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>

*Abstract of Bid as Read re: Negotiated Procurement for the Fit-out And Repair of the Subic-Clark Railway Project Management Office*

C	(use <i>Section IX, Bidding Forms</i> in case of Bid Securing Declaration) or Cash or cashier's/manager's check issued by a Universal or Commercial Bank; or Bank draft/guarantee or irrevocable letter of credit issued by a Universal or Commercial Bank (2% of ABC); or Surety Bond with a Certificate from the Insurance Commission (5% of the ABC)				
TAB D	<b>Conformity with the Technical Specifications Compliance Form</b> (Use the supplied Technical Specifications Compliance Form found in the Bid Documents as Section VII)	Passed	Blank on the compliance section (No Remarks)	Passed	Passed
TAB E	<b>Conformity with the Schedule of Requirements</b> (use <i>Section VI</i> ) duly signed in every page by the principal bidder or the bidder's authorized representative	Passed	Passed	Passed	Passed
TAB F	<b>Notarized Omnibus Sworn Statement</b> in accordance with Section 25.3 of the 2016 Revised IRR of RA 9184, and using the form prescribed in Section VIII. Bidding Forms  <b>Note:</b> The Omnibus Sworn Statement shall be accompanied by the duly notarized Special Power of Attorney,	Passed	Passed	Passed	No Submission of SPA/Partnership Resolution, or Secretary's Certificate

Abstract of Bid as Read re: Negotiated Procurement for the Fit-out And Repair of the Subic-Clark Railway Project Management Office

Handwritten signatures and initials in blue ink, including "Ju", "Jui.", "Gi", "JL", and "JL".

	Board/Partnership Resolution, or Secretary's Certificate, whichever is applicable				
<b>TAB G</b>	<b><u>Latest Audited Financial Statements</u></b> , showing, among others, the Supplier's total and current assets and liabilities, stamped "received" by the BIR or it's duly accredited and authorized institutions, for the preceding calendar year which should not be earlier than two (2) years from the date of submission of bid	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>	<b>Non Submission</b>
<b>TAB H</b>	<b><u>Computation of Net Financial Contracting Capacity (NFCC)</u></b> in accordance with ITB Clause 5 ( <i>Section IX, Bidding Forms</i> ) or a Committed Line of Credit (CLC) from a universal or commercial bank which must be at least equal to 10% of the ABC	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>	<b>Passed</b>
<b>TAB I</b>	If applicable, valid <b><u>Joint Venture Agreement (JVA)</u></b> in case the joint venture is already in existence; in the absence of a JVA, <b><u>duly notarized statements</u></b> from all the potential joint venture partners stating that they will enter into and abide by the provisions of the JVA in the event that the bid is successful, in accordance with Section 23.1(b) of the IRR.	<b>N/A</b>	<b>N/A</b>	<b>N/A</b>	<b>N/A</b>

Abstract of Bid as Read re: Negotiated Procurement for the Fit-out And Repair of the Subic-Clark Railway Project Management Office

*Jr*


*Jui.*  
*Jim*  
*Gi*  
*Je*

	<b>Other documentary requirements under RA No. 9184, as applicable:</b>				
<b>TAB J</b>	(For foreign bidders claiming by reason of their country's extension of reciprocal rights to Filipinos) <b><u>Certification from the relevant government office of their country</u></b> stating that Filipinos are allowed to participate in government procurement activities for the same item or product.	N/A	N/A	N/A	N/A
<b>TAB K</b>	<b><u>Certification from the DTI</u></b> if the Bidder claims preference as a Domestic Bidder or Domestic Entity	N/A	N/A	N/A	N/A
	<b>REMARKS</b>	<b>Passed</b>	<b>Failed</b>	<b>Passed</b>	<b>Failed</b>

Abstract of Bid as Read re: Negotiated Procurement for the Fit-out And Repair of the Subic-Clark Railway Project Management Office

<p><b>TAB L</b></p>	<p><b>Financial Proposal (ABC: Php2,850,000)</b> inclusive of all applicable taxes and fees)</p> <p>Original of duly signed and accomplished <b>Financial Bid Form</b>; and, Original of duly signed and <b>accomplished Price Schedule/s</b></p>	<p><b>Bid Price in Figure: Php2,622,000.00</b></p> <p><b>Bid Price in Words:</b></p> <p>Two Million Six Hundred Twenty Two Thousand Pesos and 00/100</p> <p>(inclusive of VAT and all applicable taxes and fees)</p>		<p><b>Bid Price in Figure: Php2,800,000.00</b></p> <p><b>Bid Price in Words:</b></p> <p>Two Million Eight Hundred Thousand Pesos and 00/100</p> <p>(inclusive of VAT and all applicable taxes and fees)</p>	
	<p><b>REMARKS</b></p>	<p><b>Lowest Bidder</b></p>		<p><b>2nd Lowest Bidder</b></p>	

**BIDS AND AWARDS COMMITTEE FOR GOODS**

  
**JOSHUA M. BINGCANG**  
 Chairperson

  
**JOCELYN L. CANIONES**  
 Vice Chairperson

  
**ATTY. RITCHIE PACLIBAR**  
 Member

  
**ATTY. CHRISTIAN T. DULDULAO**  
 Member

  
**SAMUEL JOHN D. VIDALLON**  
 Member

Observer (COA)



**IRENE JACOB**  
Observer (IASO)

# **Annex B**

**INTERNAL MEMO**

OK

FOR THE CHAIRMAN AND MEMBERS OF THE BAC FOR GOODS

**FROM : THE TECHNICAL WORKING GROUP**

**DATE : 09 November 2021**

**SUBJECT : Report on the Post Qualification Activity with the Eligible Bidder for the Negotiated Procurement for the Fit-out and Repair of Subic-Clark Railway Project Management Office**

Pursuant to the provisions in Section 34 of the Revised Implementing Rules and Regulations of RA 9184, the Technical Working Group (TWG) of the Bids and Awards Committee (BAC) for Goods conducted a post qualification evaluation on 05-08 November 2021 to determine whether the eligible bidder, **DCLABRO3 Construction**, is compliant and responsive with all the requirements and conditions in the bidding documents for the **Negotiated Procurement for the Fit-out and Repair for Subic-Clark Railway Project Management Office**.

**The post qualification activity covered the following:**

**I. Verification of the original documents**

The documents submitted, as enumerated in the Checklist of Requirements, were verified against the original copies. Based on TWG's evaluation, the documents submitted are in accordance with the requirements as they are true and faithful copies of the original documents presented during the conduct of the post qualification.

Required Documents	Remarks
PhilGEPS Certificate of Registration under Platinum Membership	<p><b>Platinum Membership</b></p> <p>PhilGEPS Reference No: 2020042159271135254802 Validity: 17-June-2022</p> <p><b>(Authentic copy as verified by the TWG)</b></p>
Registration certificate from the Department of Trade and Industry (DTI) for sole proprietorship	<p><b>DTI Certificate No. 1386926</b></p> <p>Date of Registration: 09 January 2020 Validity: 09 January 2025</p> <p><b>(Authentic copy as verified by the TWG)</b></p>



<p>Mayor's/Business permit issued by the city or municipality where the principal place of business of the prospective bidder is located.</p>	<p><b>Business/Mayor's Permit No. 0677</b>          Issued by Campesao, City of Borongan, Province of Eastern Samar          Validity: 31 December 2021   <b>(Authentic copy as verified by the TWG)</b></p>
<p>Tax clearance per E.O. 398, 2005, as finally reviewed and approved by the Bureau of Internal Revenue (BIR).</p>	<p><b>Tax Clearance Certificate</b>          TCBP No. 14-086-06-14-0576-2021-M          Validity: 14 June 2022   <b>DCLABRO3's Tax Clearance</b> was also verified with the BIR website with Sequence No. 1726, Kindly refer to the link below:   <a href="https://www.bir.gov.ph/images/bir_files/account_receivables_monitoring/FOR%20PORTAL-JUNE1-30v29.pdf">https://www.bir.gov.ph/images/bir_files/account_receivables_monitoring/FOR%20PORTAL-JUNE1-30v29.pdf</a>   <b>BIR Certificate of Registration 2303</b>          OCN-2RC 0001791615          TIN No. 408-604-954-000          Date of Registration: <b>23 May 2011</b></p>

<small>EFFECTIVE AUGUST 22, 2018, BIR HAS IMPLEMENTED THE REVENUE REGULATION NO. 18 - 2018 AMENDING SPECIFIC PROVISIONS OF REVENUE REGULATIONS NO. 8-2016 PARTICULARLY CERTAIN GUIDELINES ON THE PROCESSING OF APPLICATIONS FOR TAX CLEARANCE FOR BIDDING PURPOSES SIGNED BY CARLOS G. DOMINGUEZ, SECRETARY OF FINANCE, DATED JUNE 5, 2018.</small>									
<small>REPUBLIC OF THE PHILIPPINES          DEPARTMENT OF FINANCE          BUREAU OF INTERNAL REVENUE          RELEASED TAX CLEARANCE FOR BIDDING PURPOSES          June 1-30, 2021</small>									
SEQ. NO.	TIN	TAXPAYER'S NAME	TCC No.	DATE OF ISSUANCE			VALIDITY PERIOD		
				MM	DD	YYYY	MM	DD	YYYY
1723	924-852-331-000	LABITA, ENRICO VERANO (DENCY'S HARDWARE TOOLS & GENERAL MERCHANDISE)	TCBP No. 02 - 008 - 06-03-R0478 - 2021-M	06	03	2021	06	03	2022
1724	929-970-709-000	LABOG, IOEL FIEDACAN (HOLY ANGEL TRADING)	TCBP No. 9A - 059 - 06-01-0709 - 2021-M	06	01	2021	06	01	2022
1725	184-841-007-000	LABORTE, REYNALDO, JR V (R.V. LABORTE BUILDERS)	TCC No. 98 - 060 - 06-02-R0477 - 2021-E	06	02	2021	06	02	2022
1726	408-684-954-000	LABRO, DIOSDADO III CORPLUZ (DCLABRO3 CONSTRUCTION)	TCBP No. 14 - 86 - 06-14-0576 - 2021-M	06	14	2021	06	14	2022

## II. Performance Evaluation

To verify and evaluate the performance of the bidder, the TWG conducted performance evaluations on On-Going Contracts and Single Largest Contract declared by **DCLABRO3 Construction**, within the relevant period as provided in the Bidding Documents for purposes of determining their technical eligibility and capacity to perform contractual obligations.

<p><b>On-going Contract</b></p> <p>Statement of all its ongoing government and private contracts, including contracts awarded but not yet started, if any, whether similar or not similar in nature and complexity to the contract to be bid</p>	<p><b>Statement of All On-Going Contracts:</b></p> <p>Amount of Outstanding Contracts - <b>Php32,287,674.16</b></p> <p><b>Includes Contract with:</b></p> <p><b>1. <u>Philippines Navy, Armed Forces of the Philippines</u></b></p>
--	---

*Internal Memo: Post Qualification Report for the Negotiated Procurement for the Fit-out and Repair for Subic-Clark Railway Project Management Office - November, 2021/Version 1*

	<p><b>Supply and Delivery of Labor Materials for the Repair and Rehabilitation of MPAC Crew Barracks at NSJM</b></p> <p>Contract Duration: 90 calendar days  Date of Contract: 03 June 2021  Contract Amount: Php4,663,336.94</p> <p><i>Supported by:</i></p> <p><b>Notice of Award</b> issued 18 Dec 2020, signed by Romulo K. Vigilancia, CAPT (PN(GSC) Commanding Officer</p> <p><b>Contract Agreement</b> (PNPC-PB-SVC-01-022-21-NCEBde) between PN, AFP and DCLABRO3 Construction, notarized 03 June 2021</p> <p><b>Notice to Proceed</b> issued dated 03 June 2021, signed by Romulo K. Vigilancia, CAPT (PN(GSC) Commanding Officer</p> <p><b>Performance Evaluation:</b></p> <p><i>Not yet started due to site possession.</i></p> <p><b>Contract validation:</b></p> <p><i>The information on this project was posted on the official website of the Armed Forces of the Philippines-Philippine Navy.</i></p> <p><b><u>2. Department of Trade and Industries (DTI)</u></b></p> <p><b>Supply and Delivery of Labor and Materials, and Provision of Service for the Rehabilitation of Testing Laboratory and Warehouse of the Bureau of Philippine Standards (BPS)</b></p> <p>Contract Duration: 180 calendar days  Date of Contract: 17 June 2021  Contract Amount: Php12,241,439.70</p> <p><i>Supported by:</i></p> <p><b>Notice of Award</b> issued 27 May 2021, signed by Ireneo V. Vizmonte, Undersecretary, Head of Procuring Entity</p>
--	---

**Contract Agreement** between DTI and DCLABRO3 Construction, notarized 17 June 2021

**Notice to Proceed** issued dated 14 June 2021, signed by Neil P Catajay, Director BPS

***Performance Evaluation***

Please see the attached link for the duly accomplished Post Qualification Evaluation Form of the client:

[Post qualification DCLABRO3 Const. - sgd.pdf](#)

Department of Trade and Industries (DTI)-**Annex "A"**

**Construction Site Visit:** *DTI BPS Testing Laboratory, Salawag, Dasmarias, Cavite (with pictures attached)*

*DTI-BPS End-User: Engr. Jay Illescas and Engr Ronald Corales evaluation statements:*

- *All materials and supplies provided are within the BPS standards and came from licensed suppliers.*
- *The assigned Project Engineer is very diligent and professional in his work. Take initiative in suggesting revisions or amendments of the work for the advantage of the DTI without additional cost.*
- *In the initial months, there were delays in work due to the delayed 1st progressive payment from the client, but eventually construction was ahead of time after the payment.*
- *Overall rate is 8.5 out of 10.*
- [DTI BPS end user.jpg](#)
- [Project Site DTI BPS1.jpg](#)
- [Project Site DTI BPS2.jpg](#)
- [DCLabro3 Proj Engr and Rep.jpg](#)

**Contract Validation:**

*The details of the contract for this project was confirmed by DTI-BPS End-Users Engr. Jay Illescas and Engr. Ronald Corales*

**3. Bureau of Aquatic Resources (BFAR)**

**Construction of BFAR-NMC Fish Processing Facility at Bgy. Cagangohan, Panabo City, Davao Del Norte**

Contract Duration: 120 calendar days  
Date of Contract: 23 September 2021  
Contract Amount: Php3,003,681.02

*Supported by:*

**Notice of Award** issued 21 September 2021 signed by Eduardo B. Gongona, Head of Procuring Entity/BFAR National Director

**Contract Agreement** between BFAR and DCLABRO3 Construction notarized on 23 Sep 2021.

**Notice to Proceed** issued dated 24 Sep 2021, signed by Eduardo B. Gongona, Head of Procuring Entity/BFAR National Director

**Performance Evaluation and Contract Validation:**

[POST QUALIFICATION EVALUATION FORM.docx DC LABRO.pdf](#)

Bureau of Aquatic Resources (BFAR) - **Annex "B"**

#### **4. Government Service Insurance System (GSIS)**

##### **Rehabilitation of GSIS Tacloban Branch Office Building**

Contract Duration: 240 calendar days

Date of Contract: 26 July 2021

Contract Amount: Php23,710,475.93

*Supported by:*

**Notice of Award** issued dated 14 July 2021 signed by Atty. Dionisio C. Ebdane, Jr., Executive Vice President

**Contract Agreement** between GSIS and DCLABRO3 Construction, notarized 26 July 2021

**Notice to Proceed** issued dated 27 July 2021, signed by Atty. Dionisio C. Ebdane, Jr., Executive Vice President

**Performance Evaluation:**

[POST QUALIFICATION EVALUATION DCLABRO3 GSIS.pdf](#)

Government Service Insurance System (GSIS)-**Annex "C"**

**Contract validation:**

*The information on this project was posted on the official website of the Government Service Insurance System.*

**5. Bureau of Corrections (BuCor)**

**Construction of PDL Utility Area at Maximum Security Compound**

Contract Duration: 240 calendar days  
Date of Contract: 08 July 2021  
Contract Amount: Php23,989,538.96

*Supported by:*

**Notice of Award** issued dated 24 June 2021 signed by USEC Gerald Q. Bantag, Director General, BuCor

**Contract Agreement** (CA-INFRA-2021-006) between BUCOR and DCLABRO3 Construction, notarized 08 July 2021

**Notice to Proceed** issued dated 19 July 2021, signed by USEC Gerald Q. Bantag, Director General, BuCor

**Performance Evaluation:**

**[Post Qual Evaluation DCLabro3 BuCor.pdf](#)**

Bureau of Corrections (BuCor) - Annex "D"

**Contract validation:**

*The information on this project was posted on the official website of the Bureau of Corrections.*

<p><b>Completed Contract</b></p> <p><b><i>Statement of Single Largest Completed Contract (SLCC).</i></b> Statement of One (1) COMPLETED government and/or private contract similar in nature to the contract to be bid equivalent to at least fifty percent (50%) of the ABC completed within 5 years (21 May 2016 to 21 May 2021) prior to the deadline for the submission and receipt of bid</p> <p><b>ABC: <u>Php2,850,000.00</u></b></p>	<p><b>SLCC:</b></p> <p><b>Contract with DPWH Eastern Samar, Engineering District Office</b></p> <p><b>Rehabilitation of Multi Purpose Building (DepEd Division Office)</b></p> <p>Contract Duration: 150 days Date of Contract: February 10, 2021 Contract Amount: Php2,908,308.87</p> <p><i>Supported by:</i></p> <p><b>Notice of Award</b> issued by DPWH dated 29 January 2021, signed by Ma. Margarita Junia, District Engineer</p> <p><b>Notice to Proceed</b> issued by DPWH dated 12 February 2021, signed by Ma. Margarita Junia, District Engineer</p> <p><b>Contract Agreement</b> between DPWH and DCLABRO3 Construction</p> <p>Certificate of Acceptance issued by DepEd Division Office, Alang-Alang, Borongan City, Eastern Samar dated 26 July 2021, signed by the end user Mr. Vincent Estrella</p> <p>Various Official Receipts Issued by DCLABRO3 Construction to DPWH-Eastern Samar, District Engineering Office</p> <p>OR#0028,0029, 0040 and 0041</p> <p><b><i>Performance Evaluation and Contract Validation:</i></b></p> <p><a href="#">DPWH-DEPED EVALUATION REPORT.pdf</a></p> <p>Dept. of Public Works and Highway - <b>Annex “E”</b></p>
--	---

### III. Compliance to Technical Requirements

SPECIFICATIONS	COMPLIANCE						
<ul style="list-style-type: none"> <li>Valid PCAB License for General Engineering or General Building: Category "C", Small "B" (minimum)</li> </ul> <p><i>DCLABRO3 Construction submitted a copy of their PCAB Contractor's license 48074 for General Engineering "D", valid until June 30, 2022</i></p> <p><b>DCALABRO3 Construction</b> is included in the Registry List of Registered Contractors with a valid PCAB License as of 21 October 2021 issued by the Department of Public Works and Highways (DPWH).</p>	<p align="center"><b>Compliant</b></p>						
<ul style="list-style-type: none"> <li>Scope of Works</li> </ul> <p>Note: signed conforme in all pages of the Terms of Reference / Plans (Annex V.i and Annex "V.ii" by authorized representative/s.)</p> <p><i>DCLABRO3 Construction submitted a copy of TOR with conforme</i></p>	<p align="center"><b>Compliant</b></p>						
<ul style="list-style-type: none"> <li>Minimum Key Personnel:</li> </ul> <table border="1" data-bbox="207 1094 1003 1604"> <thead> <tr> <th data-bbox="207 1094 493 1247">Minimum Key Personnel</th> <th data-bbox="493 1094 1003 1247">Minimum Required Qualification</th> </tr> </thead> <tbody> <tr> <td data-bbox="207 1247 493 1451">Project Engineer</td> <td data-bbox="493 1247 1003 1451">PRC Registered Licensed Civil Engineer OR Architect with three (3) years in Design/Construction of Buildings or related experience</td> </tr> <tr> <td data-bbox="207 1451 493 1604">Foreman</td> <td data-bbox="493 1451 1003 1604">3 years on Repair / Construction of Bldg. or related experience</td> </tr> </tbody> </table> <p><i>The contractor's key personnel must meet the required qualifications and relevant experiences supported by their respective CVs and licenses (if applicable). The key personnel shall only be nominated to a single position.</i></p> <p><i>DCLABRO3 Construction submitted copies of CVs and valid licenses of their nominated personnels</i></p>	Minimum Key Personnel	Minimum Required Qualification	Project Engineer	PRC Registered Licensed Civil Engineer OR Architect with three (3) years in Design/Construction of Buildings or related experience	Foreman	3 years on Repair / Construction of Bldg. or related experience	<p align="center"><b>Compliant</b></p> <p align="center"><b>(<a href="#">PROJECT ENGINEER.pdf</a>)</b></p> <p align="center"><b><a href="#">DCLabro3 Civil Engr Padayao (PRC online verification).png</a></b></p> <p align="center"><b>Compliant</b></p> <p align="center"><b>(<a href="#">CONSTRUCTION FOREMAN.pdf</a>)</b></p>
Minimum Key Personnel	Minimum Required Qualification						
Project Engineer	PRC Registered Licensed Civil Engineer OR Architect with three (3) years in Design/Construction of Buildings or related experience						
Foreman	3 years on Repair / Construction of Bldg. or related experience						

<ul style="list-style-type: none"> <li>• Cost Breakdown (with signed conforme on the revised Cost breakdown as recomputed by the TWG) <a href="#">Cost Breakdown (recomputed).pdf</a></li> </ul>	<b>Compliant</b>
--	------------------

**Site visit on the On Going Project declared by the eligible bidder**

Based on the site visit conducted by TWG last November 8, 2021 at construction site for the DTI Rehabilitation of Testing Laboratory and Warehouse of the Bureau of Philippine Standards (BPS) in Dasmarias Cavite as part of their compliance to technical requirements, DCLABRO3 meet the standard construction equipment requirements as shown on the attached post qualification pictures. ([postqualpix for SCRPFit-out](#))

**IV. Financial requirement compliance.**

The eligible bidder has complied with the required financial requirements and based on our verification of their **Audited Financial Statements for Year Ended 2020** (Stamped "received" by the BIR on 29-March-2021), the following computation shows that the eligible bidder is financially liquid and in sound position to sustain the operating cash flow requirement for the transaction.

<b>COMPUTATIONS</b>	<b>DCALABRO3 Construction</b> <i>(in operation since 2011)</i>
<p style="text-align: center;"><b>NET FINANCIAL CONTRACTING CAPACITY (NFCC)</b></p> <p style="text-align: center;">Formula:</p> <p>NFCC = K (current asset – current liabilities) X 15 minus value of all outstanding works under ongoing contracts including awarded contracts yet to be started</p> <p style="text-align: center;"><i>The computation of a bidder's NFCC must be at least equal to the ABC to be bid (ABC for this Project is</i> <b><u>Php2,850,000,000</u></b></p>	<p style="text-align: center;"><b>NFCC (as computed)</b></p> <p style="text-align: center;">Current Asset - Current Liabilities x 15 (multiplier) - List of All On-going project (Outstanding)</p> <p style="text-align: center;">4,561,662.00 - 26,352.00 x 15 - 32,287,674.16</p> <p style="text-align: center;"><b>Php35,741,975.84</b></p>



<p style="text-align: center;"><b>LIQUIDITY RATIO</b></p> <p style="text-align: center;">Formula: Current Ratio = Current Assets ÷ Current Liabilities</p> <p style="text-align: center;"><i>A current ratio that is better than 1 to 1 is considered good. The higher the ratio, the better the financial position of the company.</i></p>	<p style="text-align: center;">Php 4,561,662.00 ÷ 26,352.00</p> <p style="text-align: center;"><b>Current Ratio</b> <b>173.10 to 1</b></p>
<p style="text-align: center;"><b>STATEMENT OF COMPREHENSIVE INCOME/LOSS</b></p> <p style="text-align: center;">Formula: Income Less Expenses</p>	<p style="text-align: center;"><b>Php 5,889,079.00 - 5,209,953.00</b></p> <p style="text-align: center;"><b>Net Income</b> <b>Php 679,126.00</b></p>

#### V. Other Requirements and Photo Documentation of conducted post qualification

- iv.1** The latest Income and Business Tax Returns for the **last six (6) months preceding the date of the bid submission** was also submitted by **DCALABRO3 Construction** during the conduct of the post qualification evaluation:
- Monthly Value-Added Tax Declaration (Form 2550-M);
  - Quarterly Value-Added Tax Return (Form 2550-Q); and
  - Income Tax Return (Form 1702).
- iv.2** Copy of Certificate of Registration, BIR Form 2303-OCN: 23C000179165 dated 23 May 2011 with the following line of business/industry:
- 2695 Manufacture of Articles of Concrete, Cement, Plaster
  - 4520 Building of Construction or Parts, Civil Engineering
  - 7421 Architectural, Engineering Activities and Technical
- iv.3** **DCALABRO3 Construction** is not “blacklisted” as verified in the **List of Blacklisted Suppliers/Entities** as of 07 November 2021 of GPPB’s website, see attached as **Annex “F”** ([BLACKLISTED ENTITIES-.pdf](#))
- iv.4** Photo documentation of post qualification conducted and the copies of Permits, Licenses and Clearances. See attached as **Annex “G”**.

## VI. Findings and Recommendations

The Eligible bidder - **DCLABRO3 Construction** is legally, technically, and financially capable to undertake this procurement, Hence, the TWG recommends the approval of the following:

1. To declare **DCLABRO3 Construction** as the Lowest Calculated and Responsive Bid (LCRB) for the **Negotiated Procurement for the Fit-out and Repair for Subic-Clark Railway Project Management Office**; and
2. To award the contract to **DCLABRO3 Construction** with the amount of **Two Million Six Hundred Sixteen Thousand and 90/100 Pesos only (Php 2,600,016.90)**, inclusive of VAT and all applicable taxes and fees.

**We submit the above cited information and evaluation to the Committee for consideration.**

### The Technical Working Group



**VICENTA M. NATIVIDAD**  
TWG Member

**DONALD G. TOLENTINO**  
TWG Member



**LEONOR M. RIVERA**  
Provisional Member



**JUDENE G. LAGOY**  
Provisional Member





**ALMIRA S. CLARIANES**  
Head, TWG

## Photo Documentation

**DCALABRO3 CONSTRUCTION**  
 2F DLC BLDG CIRCUMFERENTIAL ROAD, BRGY. CAMPESAO,  
 BORONGAN CITY, E. SAMAR (Main Office)  
 BAHAYANG PAG ASA, MOLINO III, BACOR, CAVITE (Satellite Office)

### Permits and Licenses

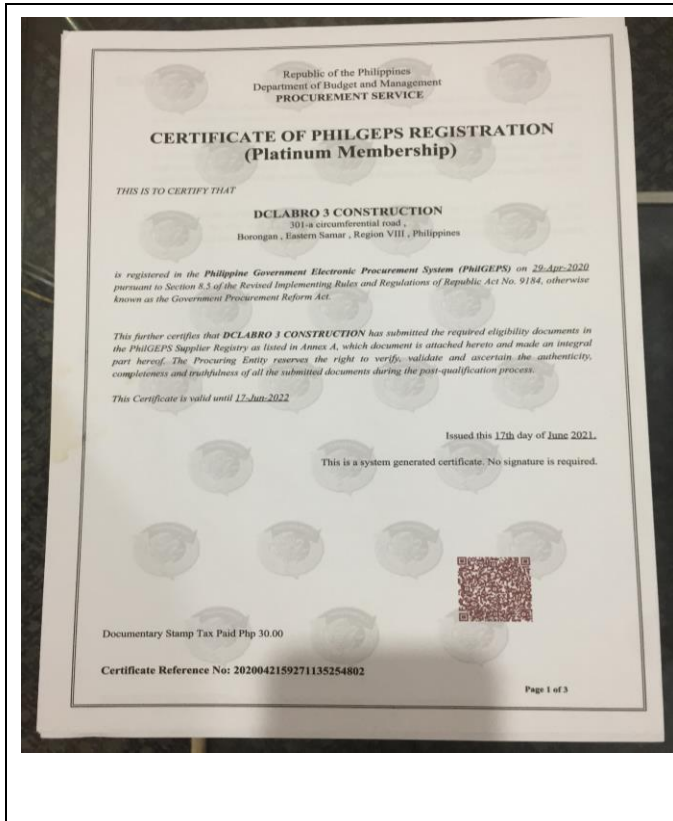

**Republic of the Philippines  
Province of Eastern Samar  
City of Torosgasan  
OFFICE OF THE CITY MAYOR  
MAYOR'S PERMIT**

To whom it may concern,  
Pursuant to the revenue code of this Municipality/City, after payment of taxes, fees and charges, etc., and compliance with existing requirements, Permit is hereby granted to the herein Taxpayer.

**DECLABRO3 CONSTRUCTION**

Business Name  
**CONSTRUCTION COMPANY/Contractors**  
Line of Business  
**Campesao, Borongan, Eastern Samar**  
Business Address

This PERMIT can be revoked anytime if any of the Conditions and Provisions set forth by the Code is Violated and /or the peace and order, health, environment, safety and security of the public are at stake:

LABRAC, DIOSDADO III CORPUZ	L-012434-000006	2021-082604000-0023
Owner's Name <b>408-684-954-000</b>	Business TIN	Permit No. <b>Renewal</b>
Jan 05 2021	DEC 31 2021	0677
Date Issued	Valid Until	Business Plate No.
		No. of Employees <b>4</b>
		Official Receipt No. <b>6148173</b>
		Official Receipt Date <b>05 Jan 2021</b>
		Annual Tax <b>7,362.84</b>
		Charge Fee <b>50.00</b>
		Mayor's Permit <b>2,000.00</b>
		Sanitary Fee <b>600.00</b>
		Signboard (Paraffex) <b>124.00</b>
		Mayor's Clearance Fee <b>50.00</b>
		Laboratory Fee <b>100.00</b>
		Occupational Fee <b>400.00</b>
		Application Fee <b>50.00</b>
		Certification Fee <b>20.00</b>
		Tax on Delivery Vehicle <b>1,230.00</b>
		Slipper <b>15.00</b>
		Annual Inspection Fee <b>120.00</b>
		Fire Inspection Fee <b>200.00</b>
		Annual Building Inspection Fee <b>120.00</b>
		<b>TOTAL</b>
		<b>12,496.84</b>
		Payment Mode <b>Quarterly</b>

**NOTES:**

- Exhibit this Permit in Your Establishment.
- This Permit is only a privilege and not a right, subject to revocation and closure of Business Establishment for any violation of existing Laws and Ordinances and conditions set forth in the Permit.
- This Permit must be renewed on or before January 20 of the following year unless sooner revoked for cause. Failure to renew within the time required shall subject the taxpayer to a surcharge of 25% of the amount of taxes, fees or charges due, plus an interest of 2% per month of the unpaid taxes, fees or charges including surcharges.
- Your Business Establishment is subject to final inspection or regulatory compliance.
- Surrender this Permit upon retirement of your Establishment.

**Jose Ivan Dikyan C. Agda**  
City Mayor

Republic of the Philippines  
DEPARTMENT OF TRADE AND INDUSTRY  
PHILIPPINE CONTRACTORS ACCREDITATION BOARD  
Nasipit City, Marikina, Philippines  
**REGULAR CONTRACTOR'S LICENSE**

FORM NUMBER: 0018

This certifies that

**DECLABRO3 CONSTRUCTION**

having complied with all the requirements for licensure pursuant to Republic Act No. 4563 (as amended) and its implementing rules and regulations, is hereby authorized to engage in the construction contracting business in the Philippines, subject to terms, conditions and provisions of license validity period, classification and category as prescribed under License Particulars in the box to the right and to the terms and conditions stipulated at the back hereof.

This further certifies that said licensee, subject to the limitations of the above-prescribed license validity period and registration validity period, kinds of project and size ranges as indicated under Registration Particulars in the box to the right hereof, is a PCAB registered contractor for government projects.

Given at Metro Manila, Philippines, on  
May 31, 2021

**HERNAN G. MATHENZO**  
Executive Director

**SEBASTIEN B. SOROME**  
Chief Secretary

DOCUMENTARY STAMP  
TAX PAID (Pp. 26.00)

CONTRACTOR'S PARTICULARS	Authorized Managing Officer <b>Rolando Cuyog Leticia III</b> Organization Type <b>Private (Region)</b> Sector <b>REGION I (Eastern Visayas)</b>
LICENSE PARTICULARS	Contractor's License Number <b>48974</b> Validity Period of the License/Renewal <b>March 16, 2020</b> Project Classification and Category <b>B</b>
REGISTRATION PARTICULARS	Registration Number <b>2020-8385</b> Registration Date <b>March 16, 2020</b> Validity Period of the Registration <b>March 16, 2020 to March 16, 2023</b> Kind of Project and Respective Size Ranges <b>Small B</b> <b>Small B</b> <b>Small B</b> <b>Small B</b> <b>Small B</b>

**IMPORTANT NOTICE: Filing schedule for license renewal application – on or before April 15, 2023**

**DEPARTMENT OF PUBLIC WORKS AND HIGHWAYS**

**List of Registered Contractors with valid PCAB License as of October 21, 2021**

Registration Name	Demarcation Address
GRAC CONSTRUCTION BUILDERS CORPORATION	002-028-7511
GRAC BUILDERS CORPORATION	
GRAC TRI-A BUILDING TRADESMAN CORPORATION (FORMERLY TRIA ENTERPRISE)	002-037-028
DAVE B. DELICADO ARCHITECTS & ASSOCIATES	002-357-9416
DAVE CONSTRUCTION	035-0162
DAMERGE CONSTRUCTION AND HEAVY EQUIPMENT SERVICES	002-357-3807
DAMAZZ TRADING CONSTRUCTION	074-0020
DAMLEY CONSTRUCTION SERVICES	002-358-942

**GOVPH**

Registration Name	Demarcation Address
DAVEY CONSTRUCTION SERVICES	002-358-942
DAMING CONSTRUCTION	002-8173
DAMORAN ENTERPRISES - CONSTRUCTION CONSTRUCTION	005-27-028058/0376212
DAMON BUILDERS	002-037-028
DAMON BUILDERS & SUPPLY	3988-407-2010
DAMP CONSTRUCTION	002-358-942
DAMP CONSTRUCTION	002-358-942
DAMP CONSTRUCTION AND SUPPLY	002-358-942
DAMP BUILDERS AND TRADING	002-358-942
DAMP CONSTRUCTION & SUPPLY	002-358-942
DAMP BUILDERS & ENTERPRISES	002-358-942
DAMP BUILDERS CORPORATION (FORMERLY DOSTERBROS CORPORATION)	074-010-0275
DAMP CONSTRUCTION	002-358-942

**REPUBLIKA NG PILIPINAS  
KAGAWARAN NG PANANALAPI  
KAWANIHAN NG RENTAS INTERNAS  
REVENUE - REGION 14  
DISTRICT 14**

BIR Form No. **2303** OCT 14  
Revised July 1997

REGISTRATION DATE: **1/23/2020**  
OCC: **ZRC001791815**

**CERTIFICATE OF REGISTRATION**

TIN	NAME	DATE
408-684-954-000	LABRAC, DIOSDADO III CORPUZ	05/23/2011

REGISTERED ADDRESS  
**301-A CIRCUMFERENTIAL RD.  
CAMPESAO BORONGAN  
EASTERN SAMAR PRD.**

REGISTERED ACTIVITIES)

TAX TYPE	REGISTRATION FEE
INCOME TAX	VALUE - ADDED TAX

TRADE NAME	LINE OF BUSINESS / INDUSTRY
DECLABRO3 CONSTRUCTION	2990 MANUFACTURE OF ARTICLES OF CONCRETE, CEMENT, PLASTER 4520 BUILDING OF CONSTRUCTION OR DAMEN, CIVIL ENGINEERING 7421 ARCHITECTURAL, ENGINEERING ACTIVITIES, TECHNICAL


**REMEMINDERS:**  
FILING OF REQUIRED TAX RETURNS TO CONFORM WITH THE ABOVE TAX TYPE/CLASSIFICATION/OPERATION TO AVOID PENALTIES

REGISTERED TAXPAYER	TIN	TYPE OF TAX	PERIOD	DATE OF FILING	W/THOLDING TAX - COMPENSATION
DECLABRO3 CONSTRUCTION	408-684-954-000	INCOME TAX	1/23/2020	1/23/2020	1/23/2020


**15737081**  
**15737091**

**THIS CERTIFICATE MUST BE EXHIBITED CONSPICUOUSLY IN THE PLACE OF BUSINESS**


*Internal Memo: Post Qualification Report for the Negotiated Procurement for the Fit-out and Repair for Subic-Clark Railway Project Management Office -November, 2021/Version 1*

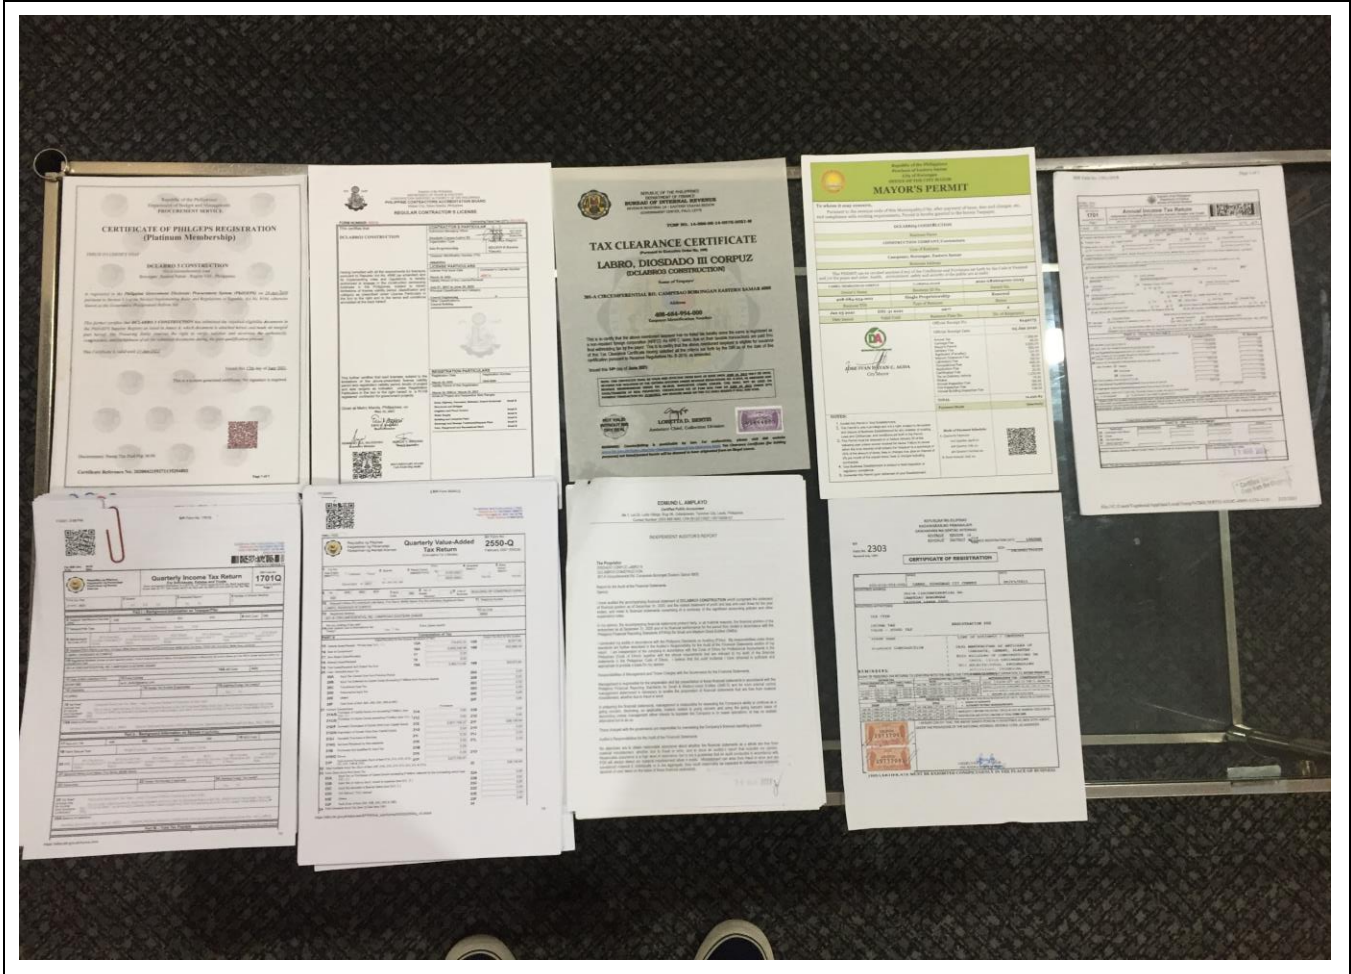


**PRESENTATION OF THE POST QUALIFICATION DOCUMENTS**

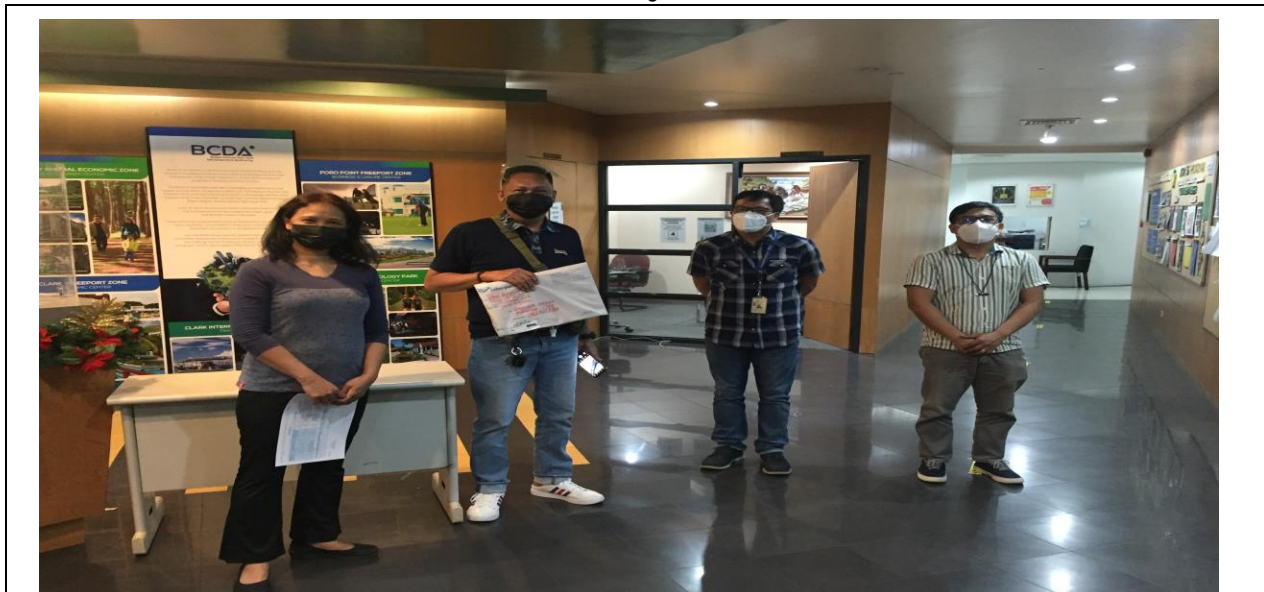

*With DCLabro3's authorized representative, Mr. Donaldito Gaspay at BCDA BTC Taguig (8-Nov-21)*

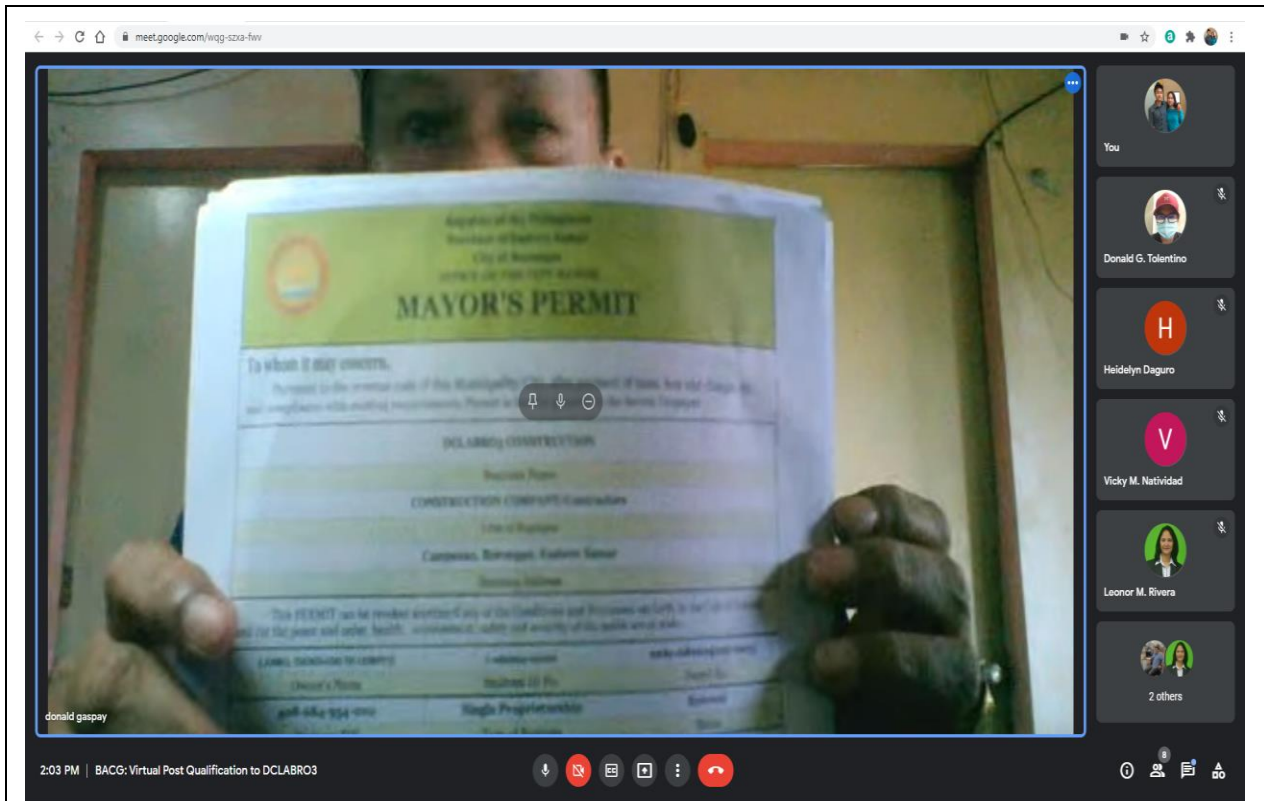

*DCLabro3's authorized representative, Mr. Donaldito Gaspay (5-Nov-21)*

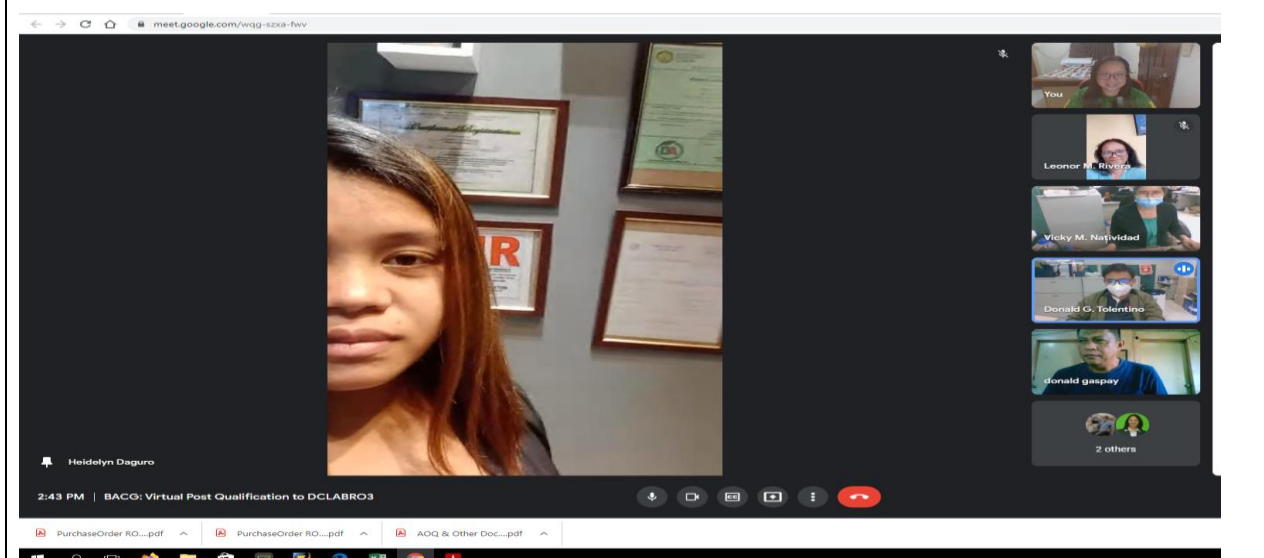

*DCLabro3's Secretary Ms. Heidelyn Daguro at Samar Office (5-Nov-21)*

## Office Facilities in Samar



*(Note: Extension office under Construction)*



**ONGOING GOVERNMENT PROJECT (Site Inspection conducted on 08 November 2021)**  
Department of Trade and Industry (DTI)- Bureau of Philippine Standard Testing Laboratory in Cavite



*With End-user's representatives, Engr. Illescas and Engr. Corales*



*With DCLabro3's representatives, Mr. Gaspay and Project Site Engr. Guialani*





REPUBLIKA NG PILIPINAS  
KAGAWARAN NG PANANALAPI  
KAWANIHAN NG RENTAS INTERNAS

REVENUE REGION 14  
REVENUE DISTRICT 86<sup>014</sup><sub>086</sub>

BIR

Form No.

**2303**


Revised July 1997

OCN:

**2RC0001791615**

BUSINESS REGISTRATION DATE: **1/23/2020**

**CERTIFICATE OF REGISTRATION**

TIN <b>408-684-954-000</b>	NAME <b>LABRO, DIOSDADO III CORPUZ</b>	DATE <b>05/23/2011</b>
REGISTERED ADDRESS <b>301-A CIRCUMFERENTIAL RD. CAMPESAO BORONGAN EASTERN SAMAR 6800</b>		
REGISTERED ACTIVITY(IES)  <b>TAX TYPE</b>  <b>INCOME TAX</b> <b>VALUE - ADDED TAX</b>  <b>REGISTRATION FEE</b>		
TRADE NAME   LINE OF BUSINESS / INDUSTRY <b>DCLABROS CONSTRUCTION</b>   <b>2695 MANUFACTURE OF ARTICLES OF CONCRETE, CEMENT, PLASTER 4520 BUILDING OF CONSTRUCTIONS OR PARTS, CIVIL ENGINEERING 7421 ARCHITECTURAL, ENGINEERING ACTIVITIES, TECHNICAL</b>		
<b>REMINDERS:</b> FILING OF REQUIRED TAX RETURNS TO CONFORM WITH THE ABOVE TAX TYPE/S WITH OR WITHOUT OPERATION TO AVOID PENALTIES		
INCOME TAX		WITHHOLDING TAX - EXPANDED
SINGLE PROPRIETOR	CORP/ PART/ ASSOC	0619E
1701Q	1702Q	1601EQ
JAN, FEB	EVERY 10 <sup>TH</sup> FF M	MAR 1 <sup>ST</sup> QTR
APR 30		APR 30
1601C	EVERY 10 <sup>TH</sup> DAY OF THE FF. MONTH	
1 <sup>ST</sup> QTR	APR 15	2 <sup>ND</sup> QTR
MAY 30		JUN 30
1604C	EVERY JANUARY 31 OF THE FF. YEAR	
2 <sup>ND</sup> QTR	AUG 15	3 <sup>RD</sup> QTR
AUG 29		OCT 30
3 <sup>RD</sup> QTR	NOV 15	NOV 29
1702	APR 15	1604E - EVERY MARCH 1 OF THE FOLLOWING YEAR
VALUE ADDED TAX		WITHHOLDING TAX - COMPENSATION
2550M	2550Q/SLSP	2551Q
JAN, FEB	EVERY 20 <sup>TH</sup> FF M	JAN, FEB, MAR
MAR 1 <sup>ST</sup> QTR	APR 25	1 <sup>ST</sup> QTR
APR, MAY	EVERY 20 <sup>TH</sup> FF M	APR, MAY, JUN
JUN 2 <sup>ND</sup> QTR	JULY 25	2 <sup>ND</sup> QTR
JULY, AUG	EVERY 20 <sup>TH</sup> FF M	JUL, AUG, SEP
SEPT 3 <sup>RD</sup> QTR	OCT 25	3 <sup>RD</sup> QTR
OCT, NOV	EVERY 20 <sup>TH</sup> FF M	OCT, NOV, DEC
DEC 4 <sup>TH</sup> QTR	JAN 25	4 <sup>TH</sup> QTR
		WITHIN 30 DAYS FROM REGISTRATION DATE OF THE FF. SHOULD BE ACCOMPLISHED:
		• BOOKS OF ACCOUNTS
		• AUTHORITY TO PRINT INVOICES/RECEIPTS
		IMMEDIATELY INFORM THIS DISTRICT OFFICE IN CASE OF TRANSFER/ CESSATION OF REGISTRATION AND OTHER CONCERNS BY FILING FORM 1905:
		<p>I HEREBY CERTIFY THAT THE ABOVE NAMED PERSON IS REGISTERED AS INDICATED ABOVE, UNDER THE PROVISIONS OF THE NATIONAL INTERNAL REVENUE CODE, AS AMENDED.</p> <p><i>Catalina P. Turla</i> CATALINA P. TURLA ASST. REVENUE DISTRICT OFFICER</p>

**THIS CERTIFICATE MUST BE EXHIBITED CONSPICUOUSLY IN THE PLACE OF BUSINESS**




Republic of the Philippines  
 DEPARTMENT OF TRADE & INDUSTRY  
 CONSTRUCTION INDUSTRY AUTHORITY OF THE PHILIPPINES  
**PHILIPPINE CONTRACTORS ACCREDITATION BOARD**  
 Makati City, Metro Manila, Philippines

**REGULAR CONTRACTOR'S LICENSE**

FORM NUMBER: **55016**

Contracting Fiscal Year (CFY): **2021/2022**

<p>This certifies that</p> <p><b>DCLABRO3 CONSTRUCTION</b></p> <p>having complied with all the requirements for licensure pursuant to Republic Act No. 4566 (as amended) and its implementing rules and regulations, is hereby authorized to engage in the construction contracting business in the Philippines, subject to herein limitations of license validity period, classification and category as prescribed under License Particulars in the box to the right and to the terms and conditions annotated at the back hereof.</p> <p>This further certifies that said licensee, subject to the limitations of the above-prescribed license validity period and registration validity period, kind/s of project and size range/s as indicated under Registration Particulars in the box to the right hereof, is a PCAB registered contractor for government projects.</p> <p>Given at Metro Manila, Philippines, on        May 31, 2021</p> <p><i>Erni G. Bagalao</i>        ERNI G. BAGALAO        Board Member</p> <p><i>Herbert G. Matienzo</i>        HERBERT G. MATIENZO        Executive Director</p> <p><i>Sergie T. Retome</i>        SERGIE T. RETOME        Board Secretary</p> <p></p> <p>DOCUMENTARY STAMP        TAX PAID (Php 30.00)</p>	<p><b>CONTRACTOR'S PARTICULAR</b></p> <p>Authorized Managing Officer <span style="float: right;">Signature <small>NOT VALID WITHOUT SIGNATURE</small></span></p> <p><b>Diosdado Corpuz Labro III</b></p> <p>Organization Type <span style="float: right;">Head Office (Region)</span></p> <p><b>Sole Proprietorship</b> <span style="float: right;"><b>REGION 8 (Eastern Visayas)</b></span></p> <p>Taxpayer Identification Number (TIN)</p> <p><b>408684954</b></p> <p><b>LICENSE PARTICULARS</b></p> <p>License First Issue Date <span style="float: right;">Contractor's License Number</span></p> <p><b>March 10, 2020</b> <span style="float: right;"><b>48074</b></span></p> <p>Validity Period of this License/Renewal</p> <p><b>July 01, 2021 to June 30, 2022</b></p> <p>Principal Classification and Category</p> <p><b>General Engineering</b> <span style="float: right;"><b>D</b></span></p> <p>Other Classification/s</p> <p><b>General Building</b>        00000000000000000000000000000000</p>														
	<p><b>REGISTRATION PARTICULARS</b></p> <p>Registration Date <span style="float: right;">Registration Number</span></p> <p><b>March 10, 2020</b> <span style="float: right;"><b>2020-0389</b></span></p> <p>Validity Period of this Registration</p> <p><b>March 10, 2020 to March 10, 2023</b></p> <p>Kinds of Project and Respective Size Ranges</p> <table border="0"> <tr> <td>Road, Highway, Pavement, Railways, Airport Horizontal</td> <td>Small B</td> </tr> <tr> <td>Structures and Bridges</td> <td></td> </tr> <tr> <td>Irrigation and Flood Control</td> <td>Small B</td> </tr> <tr> <td>Water Supply</td> <td>Small B</td> </tr> <tr> <td>Building and Industrial Plant</td> <td>Small B</td> </tr> <tr> <td>Sewerage and Sewage Treatment/Disposal Plant</td> <td>Small B</td> </tr> <tr> <td>Park, Playground and Recreational Work</td> <td>Small B</td> </tr> </table>	Road, Highway, Pavement, Railways, Airport Horizontal	Small B	Structures and Bridges		Irrigation and Flood Control	Small B	Water Supply	Small B	Building and Industrial Plant	Small B	Sewerage and Sewage Treatment/Disposal Plant	Small B	Park, Playground and Recreational Work	Small B
	Road, Highway, Pavement, Railways, Airport Horizontal	Small B													
	Structures and Bridges														
	Irrigation and Flood Control	Small B													
	Water Supply	Small B													
	Building and Industrial Plant	Small B													
	Sewerage and Sewage Treatment/Disposal Plant	Small B													
	Park, Playground and Recreational Work	Small B													

**IMPORTANT NOTICE: Filing schedule for license renewal application – on or before April 1-15, 2022**

## **TERMS AND CONDITIONS OF REGULAR LICENSE**

1. The Licensee must observe and abide by the provisions of Republic Act No. 4566, as amended by Presidential Decree No. 1746, its implementing Rules and Regulations, and other orders or instructions which the Philippine Contractors Accreditation Board shall issue from time to time pursuant to its power and authority under the law.
2. The License shall be valid during the contracting fiscal year it was issued provided it has not been suspended, cancelled, or revoked by the Board.
3. The License must be renewed annually on or before the expiration of its validity; otherwise, the contractor shall be deemed to be operating without a valid license.
4. The License is non-transferable.
5. The Licensee must not submit bids, sign construction contracts nor undertake construction projects after his/its license has expired and before the same is renewed otherwise the contractor shall be meted the appropriate disciplinary action and pay additional licensing fee in accordance with the existing schedule.
6. The Licensee's qualification is subject to review at any time to ascertain the contractor's eligibility to the present classification and category of his license.
7. License category may be upgraded and other classification(s) may be added to the license only upon formal application by the Licensee together with all the necessary supporting documents.
8. The Licensee must not undertake/implement construction projects which are not within the scope of the license's classification otherwise may be imposed appropriate disciplinary action and payment of additional licensing fee in accordance with the existing schedule.
9. The Licensee must immediately notify the Board in writing of the resignation or disassociation of its Sustaining Technical Employee and must replace the said employee within a period of ninety (90) days from the date of resignation or disassociation. Failure to notify the Board within 30 days from the date of resignation of the Sustaining Technical Employee is a ground for immediate revision of the category and classification(s) of the License.
10. Submission of falsified documents or any misrepresentation or false information in the application for a license or renewal thereof shall subject the Licensee to administrative disciplinary action without prejudice to the imposition of penal sanctions provided for by Law.
11. The Licensee must submit to the Board monitoring reports that may be required from time to time.
12. A Licensee who is retiring from the construction business must advise the Board in writing and must immediately surrender the license to the Board for cancellation.
13. The Licensee must at all times observe and adhere to the letter and spirit of the Code of Ethics of constructors.
14. The License is valid only when signed by the individual proprietor or the Authorized Managing Officer of the Licensee.
15. The Licensee must employ only licensed subcontractors and/or specialty contractors.
16. The Licensee shall sub-contract only from a licensed contractor.
17. The Licensee shall only sub-contract from a licensed project owner undertaking by himself, a project for commercial / industrial use.

## **CONSTRUCTORS' CODE OF ETHICS**

1. A constructor should be fair and honest in his business dealings, his practices and activities guided by principles of justice and equity.
2. A constructor should conduct himself with honor and dignity in his relations with his fellow constructors, fully aware that to speak maliciously of the work reputation or ability of a fellow constructor is highly unethical, and should cooperate with them for the protection and advancement of the construction industry.
3. A constructor should undertake his construction contracting activities on high ethical level and deliver quality service and faithful performance of the undertaking to which owner-clients are entitled.
4. A constructor should not advertise his firm's business in misleading terms and make false representations which may not only be improper but also immoral.
5. A constructor should refrain from the unfair competition which is a disservice to the construction industry.
6. A constructor should be fair and just to his employees, consider their welfare with sympathy and understanding.
7. A constructor should not attempt to supplant a fellow constructor who is in the employ of the owner or prevent a constructor from undertaking that which the owner has engaged him to do as it is a practice inconsistent with the honor and dignity of the construction contracting industry.
8. A constructor should hold himself dedicated to the proposition that the construction industry should be rid of participants whose reputation, conduct and practices are inimical to the construction industry.



CIVIL WORKS

- Procurement Procedures
- Bidding and Award Procedures
- Registered Contractors
- GPPB Blacklisted Entities
- Forms
- Advertisements
- Notices
- Bid Bulletin
- Abstract of Bids
- Notice of Award
- Notice to Proceed
- Awarded Contracts
- Contract Agreement
- Post-Contract Award Disclosure

## List of Registered Contractors with valid PCAB License as of October 21, 2021

Starts with

- Any -

Organization Name	Communication Address
DAVAO LIVESTRONG BUILDERS CORPORATION	082-228-7511
DAVAO SANTHONY BUILDERS CORPORATION	
DAVAO TRI-A SIBLINGS (TRIASCOR) CORPORATION (FORMERLY TRI-A ENTERPRISES)	(082)297-3226
DAVE B. RELOJERO ARCHITECTS & ASSOCIATES	(036) 267-39-69
DAVE CONSTRUCTION	839-5182
DAVERGE CONSTRUCTION AND HEAVY EQUIPMENTS RENTALS	(082) 297-3687
DAVHEZ TRADING & CONSTRUCTION	871-0435
DAVLEY CONSTRUCTION SERVICES	(082) 295-9422



CIVIL WORKS

- Procurement Procedures
- Bidding and Award Procedures
- Registered Contractors
- GPPB Blacklisted Entities
- Forms
- Advertisements
- Notices
- Bid Bulletin
- Abstract of Bids
- Notice of Award
- Notice to Proceed
- Awarded Contracts
- Contract Agreement
- Post-Contract Award Disclosure

DAVLEY CONSTRUCTION SERVICES	(082) 295-9422
DAWING CONSTRUCTION	983-0073
DAYBREAK ENTERPRISES - ENGINEERING & CONSTRUCTION	055-2712998/639173216512
DBMCC BUILDERS	09176213725
DBMR BUILDERS & SUPPLY	228-1329
DBNC CONSTRUCTION	0906 467 2010
DBP CONST. CORP.	(02) 3663684 / 3504926
DC AMBAL CONSTRUCTION AND SUPPLY	(043)7840034/(043)7417624
DC BROS BUILDERS AND TRADING	0927-932-7000
DCA CONSTRUCTION & SUPPLY	055-5009272
DCD BUILDERS & ENTERPRISES	(063)2215887/ 09177164767
DCEBUILDERS CORPORATION (FORMERLY: DCESTRANERO CORPORATION)	(074) 872-2372
<b>DCLABRO</b> 3 CONSTRUCTION	09176394014
DCMS TRADING & CONSTRUCTION	8073740
DD LIKIGAN CONSTRUCTION	0928-9172498
DD ROSAL CONSTRUCTION	043-404-8143
DDS BUILDERS	09399229724

# **COST BREAKDOWN**

Name of Project: BIDDING OF FIT-OUT AND REPAIR FOR THE SUBIC-CLARK RAILWAY PROJECT MANAGEMENT OFFICE VIA NEGOTIATED PROCUREMENT

ABC: Php2,850,000.00

**COST BREAKDOWN**

				DCLABRO3 CONSTRUCTION				
PLAN SHEET NO. REFERENCES (ANNEX V.ii)	DESCRIPTION/ SPECIFICATIONS	UNIT	QTY	UNIT	QTY	UNIT COST.	TOTAL (MATERIALS AND LABOR)	REMARKS
	<b>1. FIT-OUT AND REPAIR OF SCRP-PMO</b>							
	A MOBILIZATION / DEMOBILIZATION	LOT	1	LOT	1	60,215.68	60,215.68	
	B CONSTRUCTION / REPAIR WORKS							
A-01	1 DEMOLITION AND RELOCATION OF AFFECTED STRUCTURES	LOT	1	LOT	1	49,760.16	49,760.16	-
	2 RE-PLASTERING	SQ.M.	250				-	Price included in no. B1 as ref to detailed estimates
A-09, A-12, P-01, P-02	3 PLUMBING WORKS and WATERPROOFING			LOT	1	112,691.25	112,691.25	
	3.1 Existing Toilets (2)	LOT	1					
	3.2 Pantry	LOT	1					
	4 DOORS, WINDOWS and MIRRORS							
A-06	4.1 Doors	LOT	1	LOT	1	179,182.50	179,182.50	-
A-10	4.2 Windows	SQ.M.	202	LOT	1	52,500.00	52,500.00	-
A-10	4.3 Mirror	LOT	1	LOT	1	28,999.69	28,999.69	-
	5 FINISHES							
	5.1 Ceiling	SQ.M.	40.9				-	Price included in no. 4.3 as ref to detailed estimates
A-05, A-11	5.2 Tile Works			LOT	1	519,241.41	519,241.41	-
	5.2.1 Working Area	SQ.M.	235					
	5.2.2 Restrooms							
	Installation floor ceramic tiles	SQ.M.	12.42					
	Installation of wall ceramic tiles	SQ.M.	49.44					
A-02	5.3 Drywall Partition	SQ.M.	126.2	SQ.M.	126.2	2,491.78	314,462.64	
A-03	5.4 Low Panel Partition	SET	1	SET	1	88,797.19	88,797.19	
A-04	5.5 Glass Partition	SQ.FT.	121.11	SQ.M.	18.75	2,931.08	54,957.75	
		SQ.FT.	121.11	SQ.M.	11.25	2,931.08	32,974.65	21,983.10
					(Qty shld be 11.25 if converted to sq.m.)			Total amount of discrepancy as recomputed
A-07	5.6 Countertop	SQ.M.	18.75	LOT	1	59,774.54	59,774.54	-

CONFIRM:   
DWARIN GASPOY

Cost Breakdown (DCLABRO3 as recomputed)

Name of Project: BIDDING OF FIT-OUT AND REPAIR FOR THE SUBIC-CLARK RAILWAY PROJECT MANAGEMENT OFFICE VIA NEGOTIATED PROCUREMENT

ABC: Php2,850,000.00

### COST BREAKDOWN

				DCLABRO3 CONSTRUCTION				
PLAN SHEET NO. REFERENCES (ANNEX V.ii)	DESCRIPTION/ SPECIFICATIONS	UNIT	QTY	UNIT	QTY	UNIT COST.	TOTAL (MATERIALS AND LABOR)	REMARKS
A-07	5.7 Kitchen Cabinet	LOT	1	LOT	1	72,594.38	72,594.38	
E-01, E-02	6 ELECTRICAL WORKS			LOT	1	157,500.00	157,500.00	
	Supply and installation of electrical lightings fixtures, switches, power outlets etc.	LOT	1					
	Supply and installation of Panel Board and Circuit breaker	LOT	1					
	Supply and installation of Exhaust fans	PIECE	3					
A-08	7 PAINTING WORKS			LOT	1	300,385.31	300,385.31	
	7.1 Interior: Repainting of walls, columns and ceiling, shall be two (2) coatings	SQ.M.	365.9					
	7.2 Exterior: Repainting of walls, one (1) coating, latex paint	SQ.M.	288					
E-05	C AIR-CONDITIONING SYSTEMS (ACS)	LOT	1	LOT	1	328,125.00	328,125.00	
	1 AIRCON 2.0 Wall mounted Split-type, Inverter	UNIT	10					
E-04	D FIRE DETECTION AND ALARM SYSTEM (FDAS)	LOT	1	LOT	1	196,875.00	196,875.00	
E-03	E CONDUIT LAY-OUT FOR AUDIO-VISUAL SYSTEM	LOT	1	LOT	1	45,937.50	45,937.50	
	F OTHER EXPENSES	LOT	1			NQ	-	Price included in the total bid price
	SUB-TOTAL						2,622,000.00	
	TOTAL BID PRICE (INCLUSIVE OF ALL APPLICABLE TAXES AND FEES)						2,622,000.00	
<b>TOTAL AMOUNT AS RECOMPUTED BY TWG</b>		<b>Two Million Six Hundred Thousand Sixteen and 90/100 Pesos</b>				<b>2,600,016.90</b>		
REMARKS	DCLABRO3 has a discrepancy of Php21,983.10 from its BID PRICE							

Note: There were no costs stated in 5.1 (Ceiling) and Other Expenses in the BOW of DCLABRO3, however the bidder confirmed that its costs is inclusive of their total bid amount.

CONFIRMED:

 DADAVIDO






**POST QUALIFICATION EVALUATION FORM**  
Bids and Award Committee for Goods

Name of Bidder: **DCLABRO3 Construction**

Subject : Confirmation of Engagement for **On-Going Contracts**

<b>Name of Contract</b>	Supply and Delivery of Labor and Materials and Provision of Service for the Rehabilitation of Testing Laboratory and Warehouse of the Bureau of Philippine Standards
<b>Contract Amount</b>	Php 12,241,439.70
<b>Date of Delivery</b>	December 14, 2021
<b>Feedback on its performance:</b>	
This refers to the performance of DCLABRO3 Construction with the above-mentioned contract as satisfactory as per evaluation with its ongoing contract.	

Submitted by:

 Digitally signed by  
Michael C. Tenorio

Name/Signature: Michael C. Tenorio

Position: AO – V, HRAS GSD (Renovation and Bldg. Maintenance Section)

Date: November 8, 2021



**POST QUALIFICATION EVALUATION FORM**  
Bids and Award Committee for Goods

Name of Bidder: **DCLABRO3 Construction**

Subject : Confirmation of Engagement for **On-Going Contracts**

<b>Name of Contract</b>	CONSTRUCTION OF BFAR-NMC FISH PROCESSING FACILITY AT BRGY. CAGANGOHAN, PANABO CITY, DAVAO DEL NORTE.
<b>Contract Amount</b>	Php 3,003,681.02
<b>Date of Delivery</b>	Delivery Period 120 days
<b>Feedback on its performance:</b>	
<p><b>DCLABRO3 CONSTRUCTION is active in terms of communicating to BAC Staff with regards to paper works and they can easily requested for appearance to the office if needed.</b></p>	

Submitted by:

JENNILYN CASTILLO  
BAC STAFF  
November 8, 2021



## POST QUALIFICATION EVALUATION FORM

Bids and Award Committee for Goods

Name of Bidder: **DCLABRO3 Construction**

Subject : Confirmation of Engagement for **On-Going Contracts**

<b>Name of Contract</b>	Renovation of GSIS Tacloban Branch Office Building
<b>Contract Amount</b>	Php 23,710,475.93
<b>Date of Delivery</b>	Target Completion Date: 23 March 2021
<b>Feedback on its performance:</b>	
This is to confirm the on-going project – Renovation of GSIS Tacloban Branch Office Building. The Notice to Proceed was issued to the said contractor on 27 July 2021. Currently, we are waiting for the approval of building permit application.	


Submitted by:

**DIVINA DC APOLINAR**

OIC, Building and Maintenance Department

Government Service Insurance System

Date: 8 November 2021



**POST QUALIFICATION EVALUATION FORM**  
Bids and Award Committee for Goods

Name of Bidder: **DCLABRO3 Construction**

Subject : Confirmation of Engagement for **On-Going Contracts**

Name of Contract	Construction of PDL Utility Area at Maximum Security Compound
Contract Amount	Php 27, 989, 538. 96
Date of Delivery	July 27, 2021 (ON GOING)
Feedback on its performance:  Very Good performance.	

Submitted by:

CTM Jor-el M. De Jesus

Name/Signature

Position *Head, Planning & Design, CES*

Date *Nov. 8, 2021*



DEPARTMENT OF PUBLIC WORKS AND HIGHWAYS  
**EASTERN SAMAR**  
**DISTRICT ENGINEERING OFFICE**  
**REGIONAL OFFICE VIII**  
 Borongan City, Eastern Samar

### USER SURVEY FORM

NAME OF PROJECT: REHABILITATION OF MULTI – PURPOSE BUILDING (DEPED) DIVISION OFFICE,  
 BRGY. ALANG – ALANG, BORONGAN CITY, EASTERN SAMAR

NAME OF CONTRACTOR: DCLABRO3 CONSTRUCTION

DESCRIPTION OF WORK: REHABILITATION OF MULTI – PURPOSE BUILDING

EVALUATION CRITERIA	SATISFACTORY	BELOW SATISFACTORY	UNACCEPTABLE
<b>PROJECT DELIVERY</b> <ul style="list-style-type: none"> <li>➤ Fast response time (mobilization) ✓</li> <li>➤ Timely completion of work ✓</li> <li>➤ Adequacy of workers/ personnel assigned on site ✓</li> <li>➤ Ready provision for temporary/ back up personnel ✓</li> </ul>			
<b>WORKMANSHIP</b> <ul style="list-style-type: none"> <li>➤ Job/ service performance according to scope of work ✓</li> <li>➤ Quality of job/ service rendered ✓</li> <li>➤ Adequacy and quality of materials and supplies, tools and equipment used. ✓</li> </ul>			
<b>ATTITUDE</b> <ul style="list-style-type: none"> <li>➤ Attendance of workers/ personnel assigned ✓</li> <li>➤ Level of skills workers/ personnel assigned ✓</li> <li>➤ Personal traits of workers/ personnel assigned ✓</li> <li>➤ Cleanliness ✓</li> </ul>			

additional remarks, if any.

**OVERALL EVALUATION**

**SATISFACTORY:** ✓

**BELOW SATISFACTORY:**

**UNACCEPTABLE:**

**PREPARED BY:**

**DATE:** 02/08/21

**APPROVED BY:**

**DATE:**

  
CHRISTIAN PAUL A. BALITA

PROJECT ENGINEER

  
MA. MARGARITA C. JUNIA, D.M.

DISTRICT ENGINEER

\*Results of this survey will be used as reference for improving service performance



(transparency\_seal.php)



(https://www.foi.gov.ph)



(https://www.gppb.gov.ph/assets/pdfs/BRWFC017CAA7FB0\_010918\_split\_2.pdf)

**Disclaimer:** The ministerial authority of the GPPB and its Technical Support Office is limited only to the maintenance of the OBP, validation of requests for registration, and assistance to Procuring Entities in case of loss of access or need for updating of its account details (except for agency name and official e-mail address) after registration. Hence, posting and updating of status of blacklisted entities are vested within the procuring entity.

**Questions and clarifications must be directed towards the PE who posted the blacklisting order.**

Search by Procuring Entity or Blacklisted Entity






## BLACKLISTED ENTITIES

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
1	A. S. AQUA-AGRI PRODUCTS AND ENTERPRISES	PHILIPPINE CARABAO CENTER	SUPPLY AND DELIVERY OF CROSSBRED/PUREBRED BUFFALOES (250 HEADS) REBID PCC-USM	16 Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2020-11-10 - 2021-11-09
2	Vinhar Construction and Marketing	Bataan General Hospital and Medical Center	Construction of Five-Storey Multi-Specialty Building (Phase II)	1. Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract; 2. Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Quality of materials and workmanship not complying with the approved specifications; and 3. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2020-11-27 - 2021-11-26

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
3	Benguet Builders	DEPARTMENT OF TRANSPORTATION	Construction of the Covered Walkway in the DOTr Compound	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2020-11-28 - 2021-11-28
4	B.C. Cuerpo Construction Corporation	Zamboanga City State Polytechnic College	1) Construction of Engineering Building	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-01 - 2021-11-30
5	B.C. Cuerpo Construction Corporation	Zamboanga City State Polytechnic College	Refitting of Garments and Textile Shop Laboratory Classrooms	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-01 - 2021-11-30
6	WELMARY CONSTRUCTION AND SUPPLY	DEPARTMENT OF TRANSPORTATION	RENOVATION OF DOTr CANTEEN	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2020-12-01 - 2021-12-01
7	WELMARY CONSTRUCTION AND SUPPLY	DEPARTMENT OF TRANSPORTATION	PROPOSED STORAGE EXTENSION OF DOTr CLARK OFFICES (2523, 2528, 2529 AND 2532)	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2020-12-01 - 2021-12-01
8	Biclat Agrarian Reform Multi-Purpose Cooperative	Department of Education - National Capital Region	Supply and Delivery of School Furniture under the CY 2018 Basic Education Facilities Fund	Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2020-12-01 - 2021-12-01



#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
9	Bongabong Coconut Farmers Multi-Purpose Cooperative	Department of Education - National Capital Region	Supply and Delivery of School Furniture under the CY 2018 Basic Education Facilities Fund	Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2020-12-01 - 2021-12-01
10	Bongabong Coconut Farmers Multi-Purpose Cooperative	Department of Education - National Capital Region	Supply and Delivery of TVL Tools and Equipment	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-01 - 2021-12-01
11	Sitio Caldo Multi-Purpose Cooperative	Department of Education - National Capital Region	Supply and Delivery of School Furniture under the CY 2018 Basic Education Facilities Fund	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-01 - 2021-12-01
12	CJDS Enterprise	Procurement Service - Department of Budget and Management	Supply and Delivery of Various Janitorial Supplies for the Procurement Service under Public Bidding No. 18-270-7	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-23 - 2021-12-23
13	911 Alarm, Inc.	Procurement Service - Department of Budget and Management	Supply and Delivery of Fire Coats and Trousers for the Bureau of Fire Protection under Public Bidding No. 16-098-3	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-23 - 2021-12-23
14	Joint Venture of Integrated Energy Systems & Resources, Inc. and Unimasters Conglomeration Incorporated	Procurement Service - Department of Budget and Management	Supply and Delivery of Testing Kits for COVID-19 Response for the Department of Health (DOH) under RFO No. MDC-RFO-20-03-91	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2020-12-23 - 2021-12-23

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
15	Tomas B. Binbinon, Jr., Project Manager, Sharysu Builders and Marketing	Nueva Vizcaya State University (NVSU)	Construction of Training Center Annex Building (Bayombong Campus)	a.) Incurrence of a negative slippage of 33.76% in the completion of the work, after the contract time has expired due to the contractor's fault; and b.) Failure of the contractor to execute the works in accordance with the contract, and persistently or frankly neglecting to carry out its obligations under the contract.	Two (2) Years Blacklisting	2019-12-26 - 2021-12- 25
16	Tomas B. Binbinon, Jr., Project Manager, Sharysu Builders and Marketing	Nueva Vizcaya State University (NVSU)	Repair of Existing REBD Left Wing (Bayombong Campus)	a.) Incurrence of a negative slippage of 51.98% in the completion of the work, after the contract time has expired due to the contractor's fault; and b.) Failure of the contractor to execute the works in accordance with the contract, and persistently or frankly neglecting to carry out its obligations under the contract.	Two (2) Years Blacklisting	2019-12-26 - 2021-12- 25
17	BERLYN ENTERPRISES	PHIIPPINE COAST GUARD	Supply, Delivery and Installation of Nineteen (19) Lighted Navigational Buoys in Toledo Port, Roxas Port and Kalayaan Group of Islands	a) Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract; b) Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2021-01-14 - 2022-01- 14
18	INFINITE POWERTECH SCIENTIFIC EQUIPMENT SALES	DEPARTMENT OF EDUCATION REGIONAL OFFICE 3	Supply, Delivery, Installation, Testing, Commissioning and Training for Various Tools and Equipment for Region III Technical-Vocational-Livelihood (TVL) Programs of TVL Senior High Schools - Lot 4 (Beauty and Wellness Machines)	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2021-01-18 - 2022-01- 18
19	A.C. Ong Consulting Inc.	Subic Bay Metropolitan Authority	Consultancy Services for the Preparation of Detailed Engineering Design for Various Tourism Projects	Poor performance by the consultant of his services arising from his fault or negligence – Defective design resulting in substantial corrective works in design and/or construction.	One Year Blacklisting	2021-01-21 - 2022-01- 21

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
20	ITP Construction, Inc., Guangxi Hydroelectric Construction Bureau Co.,	National Irrigation Administration - Central Office	Contract No. R3-BBMPIID-C-6, Construction of Balog-Balog Storage Dam and its Appurtenant Structures under the Balog-Balog Multipurpose Project - Phase II	14. Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 35. Grounds for Termination of Contracts under Annex "I" of the Revised IRR of RA 9184. The Contractor does not actually have on the project site the minimum essential equipment listed on the Bid necessary to prosecute the works in accordance with the approved work plan and equipment deployment schedule as required for the project.	One Year Blacklisting	2021-01-28 - 2022-01-27
21	Joint Venture of ARN Builders Inc. and IServe Customer Management Solutions (ISERVE) Inc., ARN Builders Inc, IServe Customer Management Solutions (ISERVE) Inc	University of the Philippines	Construction of UP Diliman Swimming Pool and Stadium.	1) Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 2) Assignment and subcontracting of the contract or any part thereof or substitution of key personnel named in the proposal without prior written approval by the procuring entity. 3) Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause. 4) Other violation: (Specify) Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the Performance Rating of the Project Management Office of the University of the Philippines - Negative slippage of 15%.	One Year Blacklisting	2021-02-03 - 2022-02-03

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
22	GREEN ASIA CONSTRUCTION AND DEVELOPMENT CORPORATION	National Irrigation Administration - Central Office	Contract No. CMIPP2-C-U4R Rehabilitation / Improvement of Lateral "C" (Sta. 8+955.90 - Sta. 13+902.95), Lateral "C" Extension (Sta. 0+000 - Sta. 17+412.37) Lateral "Cx-3" and Construction /or Modification of Related Structures Including Fabrication, Supply, Delivery, Installation and Commissioning of Steel Gates	14. Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 35. Grounds for Termination of Contracts under Annex "I" of the Revised IRR of RA 9184. The Contractor incurred negative slippage of fifteen percent (15%) or more in accordance with Presidential Decree 1870	One Year Blacklisting	2021-02-08 - 2022-02- 07

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
23	Kaisa Consulting Company, Inc. and Polaris Consulting and Services Limited	Development Bank of the Philippines	Procurement, Customization and Implementation of an Integrated Core Banking Solution for the Development Bank of the Philippines	14 Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 15 Assignment and subcontracting of the contract or any part thereof or substitution of key personnel named in the proposal without prior written approval by the procuring entity. 16 Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract. 17 Poor performance by the consultant of his services arising from his fault or negligence - Defective design resulting in substantial corrective works in design and/or construction. 18 Poor performance by the consultant of his services arising from his fault or negligence - Failure to deliver critical outputs due to consultant's fault or negligence. 19 Poor performance by the consultant of his services arising from his fault or negligence - Specifying materials which are inappropriate, substandard, or way above acceptable standards. 23 Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause. 24 The contractor has engaged, before or during implementation of the contract, in unlawful deeds and behaviors relative to contract acquisition and implementation as enumerated in Section III.D. of the Guidelines on Termination of Contracts.	One Year Blacklisting	2021-02-16 - 2022-02-15

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
24	TJTF Trading	University of the Philippines	Supply and Delivery of Ten (10) Units Branded Laptop	1) Failure of the contractor, due solely to his fault or negligence, to mobilize and start work or performance within the specified period in the Notice to Proceed ("NTP"). 2) Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 3) Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2021-02-16 - 2022-02-15
25	Infinite Powertech Scientific Equipment Sales	Department of Education - Schools Division of Negros Oriental	FY 2018 Provision of Tools and Equipment for TVL Programs of TVL SHS, Lots 1 to 4	a. Failure of the contractor, due solely to his fault or negligence, to mobilize and start work or performance within the specified period in the Notice to Proceed ("NTP"); and b. Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2021-03-04 - 2022-03-04
26	Apo Philtrade and Trading Services, Inc. (APTSI)	Philippine Navy	Continuous Maintenance Availability (CMAV) of LS551	Termination of the contract in part due to default pursuant to section III (A)(a), Annex I, RIRR of RA 9184 (Guidelines on the Termination of Contract)	Two (2) Years Blacklisting	2020-03-18 - 2022-03-18
27	JO Builders	Office of the ACofAS for Logistics, A-4, Headquarters Philippine Air Force, Armed Forces of the Philippines	PAF Contract Nr PAFPC-CDS-18-231, for the Repair and Renovation of BOQ-1 #9004-01 at EAAB in the amount of Four Million One Hundred Fifteen Thousand Pesos only (PhP4,115,000.00).	The contractor abandoned the project and with an accumulated negative slippage of 98.909%.	Two (2) Years Blacklisting	2020-03-19 - 2022-03-19
28	ANISCO CONSTRUCTION & SUPPLY	Philippine Science High School - MIMAROPA Region Campus	Implementation of the Project: Construction of Sports Facilities, Implementation of the Project: Site Development	Submission of eligibility requirements containing false information or falsified documents. Submission of Bids that contain false information or falsified documents, or the concealment of such information in the Bids in order to influence the outcome of eligibility screening or any other stage of the public bidding.	One Year Blacklisting	2021-03-24 - 2022-03-24

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
29	Blackwater Philippines Security Solutions Inc.	Authority of the Freeport Area of Bataan	Security Services for AORs I -V	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2021-04-05 - 2022-04-04
30	TWIN DRAGON CONSTRUCTION	Philippine Science High School - MIMAROPA Region Campus	Implementation of the Project: Site Development	Submission of eligibility requirements containing false information or falsified documents. Submission of Bids that contain false information or falsified documents, or the concealment of such information in the Bids in order to influence the outcome of eligibility screening or any other stage of the public bidding.	One Year Blacklisting	2021-04-28 - 2022-04-28
31	LICHT INDUSTRIAL CORPORATION	PHILIPPINE AIR FORCE PRpOCUREMENT CENTER	PAFPC-CDS-20-126 Procurement of Generators Set Type	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2021-05-14 - 2022-05-14
32	Zarepath Construction and Supply	Bureau of Jail Management and Penology - Region V	Construction of Jail Building at Masbate City Jail	1. Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%; and 2. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2021-06-28 - 2022-06-28
33	Herbana Builders and Supply	Bureau of Jail Management and Penology - Region V	Construction of Jail Building Annex Phase 2 at Naga City District Jail	-Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet- Negatice Slippage of 15%; and - Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2021-07-08 - 2022-06-28

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
34	Herbana Builders and Supply	Bureau of Jail Management and Penology - Region V	Construction of Jail Building Annex at Pioduran Municipal Jail	1. Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet- Negative Slippage of 15%; and 2. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2021-07-08 - 2022-06-28
35	Stone of David Corp., Montenegro Defence Industry	Philippine National Police - Special Action Force	Supply and Delivery of 3,600 Rounds 40mm Ammunition for Grenade Launcher	14 and 16	One Year Blacklisting	2021-07-01 - 2022-07-01
36	CDJ BULIDERS & CONSTRUCTION SUPPLIES	BUREAU OF FIRE PROTECTION-NATIONAL CAPITAL REGION	REPAIR/IMPROVEMENT OF PATEROS MUNICIPAL FIRE STATION (PHASE II), NCR	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract; Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%; and Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2021-07-07 - 2022-07-07
37	Stone of David Corp., Excalibur Army SPOL. S.R.O	Philippine National Police - Special Action Force	Supply and Delivery of 148 Units Multi Grenade Launcher (MGL) Rounds 40mm Ammunition for Grenade Launcher	14 and 16	One Year Blacklisting	2021-07-13 - 2022-07-13
38	Stone of David Corp., Excalibur Army SPOL. S.R.O	Philippine National Police - Special Action Force	Supply and Delivery of 26 Units Rocket Launcher with Basic Load	14 and 16	One Year Blacklisting	2021-07-13 - 2022-07-13



#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
39	J. Corpuz Builders	University of the Philippines	Proposed Renovation of Fonacier Hall Phase 2	1. Failure of the contractor, due solely to his fault or negligence, to mobilize and start work or performance within the specified period in the Notice to Proceed ("NTP"). 2. Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 3. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause. 4. The contractor has engaged, before or during implementation of the contract, in unlawful deeds and behaviors relative to contract acquisition and implementation as enumerated in Section III.D. of the Guidelines on Termination of Contracts.	One Year Blacklisting	2021-07-15 - 2022-07-14
40	Fix and Care Ref and Aircon Services, Inc.	University of the Philippines	Supply Delivery, Installation, Testing and Commissioning of Air-conditioning Units	1) Failure of the contractor, due solely to his fault or negligence, to mobilize and start work or performance within the specified period in the Notice to Proceed ("NTP"). 2) Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 3) Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause. 4) The contractor has engaged, before or during implementation of the contract, in unlawful deeds and behaviors relative to contract acquisition and implementation as enumerated in Section III.D. of the Guidelines on Termination of Contracts.	One Year Blacklisting	2021-08-05 - 2022-08-04

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
41	Lakas Agritech Marketing	Office of Civil Defense	Supply and Delivery of Emergency Shelter Materials (Tarpaulin)	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2021-08-11 - 2022-08-10
42	DUBC CONST CORP.	LGU-General Santos City	19CW-GSC-038 Road Concreting of National Hi-way to Purok Estrella, Barangay Calumpang, General Santos City	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2021-08-17 - 2022-08-16
43	ISULAN ECT CONSTRUCTION & GEN. MERCHANDISE INC.	LGU-General Santos City	18NCW-GSC-002 REHABILITATION / IMPROVEMENT OF WATER SYSTEM AT HALL OF JUSTICE, BRGY. LAGAO, GENERAL SANTOS CITY	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2021-08-24 - 2022-08-23
44	IYADA BUILDERS AND ENTERPRISES	LGU-General Santos City	18CW-GSC-060 CONSTRUCTION OF FOUNDING MAYORS LANDMARK, JUNCTION OF SANTIAGO BLVD., ROYECA BLVD., P. ACHARON BLVD., IN BRGY. BULA AND BRGY. DAD. SOUTH, GENERAL SANTOS CITY	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2021-08-24 - 2022-08-23
45	JTA Builders	Aklan State University	3-STOREY TOURISM DEVELOPMENT CENTER BUILDING AT ASU-IBAJAY CAMPUS	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause. Negative slippage of 192.50% as of September 2, 2019. Non-deployment of committed equipment listed in the Bid and in accordance with the approved work plan and equipment deployment schedule.	Two Year Blacklisting	2020-08-28 - 2022-08-27

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
46	Markmedia Solutions.com	PhilHealth Regional Office CAR	Procurement of Various PhilHealth Collaterals per Job Order No. J-20-006 dated October 26, 2020	Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2021-09-06 - 2022-09-05
47	AMAZING FIND BUILDERS CORPORATION	LGU-General Santos City	19CW-GSC-033 CONSTRUCTION OF WATER SYSTEM WITH DISTRIBUTION PIPELINE AT BALUAN ELEMENTARY SCHOOL, BRGY. BALUAN, GENERAL SANTOS CITY (RE-BID)	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2021-09-08 - 2022-09-07
48	JAMI CONSTRUCTION AND SUPPLY	LGU-General Santos City	(2FB)N19-10-064 / N2019-10-313 CONTAINER VAN-40 FOOTER	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.	One Year Blacklisting	2021-09-13 - 2022-09-12
49	Stone of David Corp., GAIA Automotive Industries Limited	Philippine National Police - Special Action Force	One (Lot) MPAV Armored Personnel Carrier and Accessories	14 and 16	One Year Blacklisting	2021-09-15 - 2022-09-15
50	Square Meter Trading and Construction Corporation (SMTCC)	Philippine Science High School - Main Campus	Construction of Academic Building for Senior High Program	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2021-10-06 - 2022-10-05
51	Fatin Enterprise	Department of Environment and Natural Resources - National Capital Region	Procurement of Office Furniture and Portable Generator Set	Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2021-10-05 - 2022-10-06
52	Fatin Enterprise	Department of Environment and Natural Resources - National Capital Region	Procurement of Office Furniture and Portable Generator Set	Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2021-10-05 - 2022-10-06

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
53	PTWO Builders / PTWO Construction Services	Department of Environment and Natural Resources - National Capital Region	Contract Agreement for the Construction of Five (5) Green House at Department of Environment and Natural Resources – National Capital Region (DENR-NCR) Production Nursery	Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract.	One Year Blacklisting	2021-10-05 - 2022-10-06
54	LSV Global Ventures Inc.	Philippine National Police - Special Action Force	Supply and Delivery of 40 Units Parachute under Contract No. SAF 2018-64	14 Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 16 Unsatisfactory progress in the delivery of the goods by the manufacturer, supplier or distributor arising from his fault or negligence and/or unsatisfactory or inferior quality of goods, as may be provided in the contract. 35 Other violation specified under: Annex I of the Revised IRR of RA 9184 para a. provides that "the Procuring Entity" shall terminate a contract for default when any of the following: a. Outside Force Majeure the supplier fails to deliver or perform any or all of the goods within the period(s) specified in the contract, or with in any extension thereof granted by the Procuring Entity pursuant to a request made by the supplier prior to the delay, and such failure amounts to at least ten percent (10%) of the contract price	One Year Blacklisting	2021-10-07 - 2022-10-07
55	UYG CONSTRUCTION, INC.	Province of Antique	IB No. K-2020-025 (SC) Construction of Multi-purpose Center/Evacuation Center, etc.	1. Submission of eligibility requirements containing false information or falsified documents. 2. Submission of Bids that contain false information or falsified documents, or the concealment of such information in the Bids in order to influence the outcome of eligibility screening or any other stage of the public bidding.	Two Year Blacklisting	2020-10-15 - 2022-10-15

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
56	JOINT VENTURE OF A. HAE TRAFFIC AND COLISEUM FACILITIES, INC. and KANGNAM CHEMICAL COMPANY, LTD.	University of the Philippines	Supply and Installation of the University of the Philippines Diliman Synthetic Running Track	1) Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract.; 2) Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2021-10-20 - 2022-10-19
57	LABX CORPORATION	University of the Philippines	Supply and Delivery of One (1) Lot Hot Plate	1) Failure of the contractor, due solely to his fault or negligence, to mobilize and start work or performance within the specified period in the Notice to Proceed ("NTP"), 2) Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract; and 3) Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	One Year Blacklisting	2021-10-28 - 2022-10-27
58	Universal Harvester, Inc.	Department of Agriculture - Regional Field Office, Cordillera Administrative Region	Supply and Delivery of Fertilizers under IB No. 2021-01 amounting to Php7,474,625.00 with Notice to Proceed dated March 5, 2021	Failure to deliver the remaining 4,200 bags of fertilizers under their contract which they have requested for termination due to escalating prices in the market vs the contract amount.	Two Year Blacklisting	2021-10-29 - 2022-10-28
59	GRANBY TRADING & CONSTRUCTION	LGU-General Santos City	17CW-GSC-086 CONSTRUCTION OF OFFICE BUILDING OF C.E.O, BRGY. BULA, GENERAL SANTOS CITY	Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 15%.	One Year Blacklisting	2021-11-02 - 2022-11-01

#	Blacklisted Entity	Procuring Entity	Project	Offense/s	Sanction/s	Period of Suspension
60	JTA BUILDERS, INC	Aklan State University	Construction of Library and Information Center Building	1. Failure by the contractor to fully and faithfully comply with its contractual obligations without valid cause, or failure by the contractor to comply with any written lawful instruction of the procuring entity or its representative(s) pursuant to the implementation of the contract. 2. Poor performance by the contractor or unsatisfactory quality and/or progress of work arising from his fault or negligence as reflected in the CPES rating sheet - Negative slippage of 230% as of July 8, 2020. 3. Willful or deliberate abandonment or non-performance of the project or contract by the contractor resulting to substantial breach thereof without lawful and/or just cause.	Two Year Blacklisting	2020-11-12 - 2022-11-11
61	HF Enterprises	Bureau of Fire Protection Region 6	Construction of San Jose Fire Station Building; and Construction of Barotac Viejo Fire Station Building	Submission of eligibility requirements containing false information or falsified documents; and Submission of Bids that contain false information or falsified documents, or the concealment of such information in the Bids in order to influence the outcome of eligibility screening or any other stage of the public bidding.	Two Year Blacklisting	2020-12-01 - 2022-11-30
62	MMEEN Construction	Department of Budget and Management	Replacement of Tiles and Repainting of the Interior Walls and Finishes of Budget Information Training Service Office	Submission of Bids that contain false information or falsified documents, or the concealment of such information in the Bids in order to influence the outcome of eligibility screening or any other stage of the public bidding.	Two Year Blacklisting	2021-03-10 - 2023-03-10
63	MMEEN Construction	Department of Budget and Management	Replacement of Tiles and Repainting of the Interior Walls and Finishes of Budget and Management Bureau-B Office	Submission of Bids that contain false information or falsified documents, or the concealment of such information in the Bids in order to influence the outcome of eligibility screening or any other stage of the public bidding.	Two Year Blacklisting	2021-03-24 - 2023-03-23
64	See Manufacturing Contractor	Department of Budget and Management	Supply and Delivery of Furniture and Fixtures for the DBM Arcache Building	Failure, refusal, or unable to post the required Performance Security within the period stipulated in the 2016 Revised IRR of Republic Act No. 9184	Two Year Blacklisting	2021-05-27 - 2023-05-26

## REPUBLIC OF THE PHILIPPINES

- Official Gazette
- Office of the President
- Official Directory
- Official Calendar



## EXECUTIVE

- Office of the President
- Office of the Vice President
- Department of Education
- Department of Interior and Local Government
- Department of Finance
- Department of Health
- Department of Science and Technology
- Department of Trade and Industry

## LEGISLATIVE

- Senate of the Philippines
- House of Representatives

## JUDICIARY

- Supreme Court
- Court of Appeals
- Sandiganbayan
- Court of Tax Appeals
- Judicial Bar and Council

## SITE ANALYTICS

# NOMINATED PERSONNELS



**KEY PERSONNEL  
(FORMAT OF BIO-DATA)**

Give the detailed information of the following personnel who are scheduled to be assigned as full-time field staff for the project. Fill up a form for each person.

- Authorized Managing Officer / Representative: **DONALDITO P. GASPAY**
- Sustained Technical Employee

1. Name : **Engr. VICENTE P. PADAYAO JR.**
2. Date of Birth : 12/19/1962
3. Nationality : Filipino
4. Education and Degrees : BS in Civil Engineering
5. Specialty : General Building and General Engineering
6. Registration : PRC License No. **0050445**
7. Length of Service with the Firm : 6 Years From January (Months) 2015 to (Years) To Present
8. Years of Experience : 33 Years

9. If Item 7 is less than ten (10) years, give name and length of service with previous employers for a ten (10)-year period (attached additional sheet/s), if necessary:

Name and Address of Employer

Length of Service

3G & A CONSTRUCTION & SUPPLY <b>Ilocos</b>	:	12 Year(s) from 1988 to 2000
3J CONSTRUCTION <b>Quezon city</b>	:	5 Year(s) from 2000 to 2005
ESR CONSTRUCTION DEVELOPMENT CORP. <b>Pagadian</b>	:	5 Year(s) from 2005 to 2010
GREAT ZONE ENTERPRISES <b>Benguet</b>	:	5 Year(s) from 2010 to 2015
DCLABRO3 CONSTRUCTION <b>Borongan City</b>	:	6 Year(s) from 2015 to Present


10. Experience

This should cover the past ten (10) years of experience. (Attached as many pages as necessary to show involvement of personnel in projects using the format below).

1. Name	:	Construction of Loom River Front Park at Brgy. Taboc, Borongan City, Eastern Samar
---------	---	--

" Certified True Machine  
Copy from Original

2.	Name and Address of Owner	:	LGU – BORONGAN/City Hall, Borongan City
3.	Name and Address of the Owner's Engineer (Consultant)	:	Engr. LUCITO R. AFABLE/Borongan City Eastern Samar
4.	Indicate the Features of Project (particulars of the project components and any other particular interest connected with the project)	:	Construction of Loom River Front Park at Brgy. Taboc, Borongan City, Eastern Samar
5.	Contract Amount	:	Php 13,240,102.05
6.	Position	:	Project Engineer
7.	Structures for which the Employee was Responsible	:	Building Construction
8.	Assignment Period	:	From September (Months) 2020 (Years) to April (Months) 2021 (Years)

  
**Engr. VICENTE P. PADAYAO JR.**  
 Name and Signature of Employee

It is hereby certified that the above personnel can be assigned to this project, if the contract is awarded to our company.

**Borongan City – October 28, 2021**  
 (Place and Date)

  
**DONALDITO R. GASPAY**  
 The Authorized Representative

" Certified True Machine Copy from Original "

# PROJECT ENGINEER

Republic of the Philippines  
**PROFESSIONAL REGULATION COMMISSION**  
PROFESSIONAL IDENTIFICATION CARD





LAST NAME	▶	<b>PADAYAO</b>
FIRST NAME	▶	<b>VICENTE JR</b>
MIDDLE NAME	▶	<b>P</b>
REGISTRATION NO.	▶	<b>0050445</b>
REGISTRATION DATE	▶	<b>06/15/1987</b>
VALID UNTIL	▶	<b>12/19/2024</b>

**CIVIL ENGINEER**



Professional Regulation Commission  
www.prc.gov.ph

**CERTIFICATION**

20-3464454

This is to certify that the person whose name, photograph, and signature appear herein is a duly registered professional, legally authorized to practice his/her profession with all the rights and privileges appurtenant thereto.


This is to certify further that he/she is a professional in good standing and that his/her certificate of registration/professional license has not been suspended, revoked or withdrawn.

  
TEOFILO S. PILANDO, JR.  
Chairman

Signature of Professional

C-20

"Certified True Machine Copy from the Original"



**KEY PERSONNEL  
(FORMAT OF BIO-DATA)**

Give the detailed information of the following personnel who are scheduled to be assigned as full-time field staff for the project. Fill up a form for each person.

- Authorized Managing Officer / Representative: **DONALDITO P. GASPAY**
- Sustained Technical Employee

1. Name : **JESUS G. CATIGHUD**

2. Date of Birth : 12/27/1968

3. Nationality : Filipino

4. Education and Degrees : High School Graduate

5. Specialty : General Building and General Engineering

6. Registration : N/A.

7. Firm : Length of Service with the Firm : 6 Years From January (Months) 2015 (Years) To Present

8. Years of Experience : 21 years


9. If Item 7 is less than ten (10) years, give name and length of service with previous employers for a ten (10)-year period (attached additional sheet/s), if necessary:

<u>Name and Address of Employer</u>	<u>Length of Service</u>
3G & A CONSTRUCTION & SUPPLY <b>Ilocos</b>	: 12 Year(s) from 1988 to 2000
3J CONSTRUCTION <b>Quezon city</b>	: 5 Year(s) from 2000 to 2005
ESR CONSTRUCTION DEVELOPMENT CORP. <b>Pagadian</b>	: 5 Year(s) from 2005 to 2010
GREAT ZONE ENTERPRISES <b>Benguet</b>	: 5 Year(s) from 2010 to 2015
DCLABRO3 CONSTRUCTION <b>Borongon City</b>	: 6 Year(s) from 2015 to Present

10. Experience

This should cover the past ten (10) years of experience. (Attached as many pages as necessary to show involvement of personnel in projects using the format below).

1. Name	:	Construction of Loom River Front Park at Brgy.
---------	---	--

" Certified True Machine Copy from the 

			Taboc, Borongan City, Eastern Samar
2.	Name and Address of Owner	:	LGU – BORONGAN/City Hall, Borongan City
3.	Name and Address of the Owner's Engineer (Consultant)	:	Engr. LUCITO R. AFABLE/Borongan City Eastern Samar
4.	Indicate the Features of Project (particulars of the project components and any other particular interest connected with the project)	:	Construction of Loom River Front Park at Brgy. Taboc, Borongan City, Eastern Samar
5.	Contract Amount	:	Php 13,240,102.05
6.	Position	:	Foreman
7.	Structures for which the Employee was Responsible	:	Building Construction
8.	Assignment Period	:	From September (Months) 2020 (Years) to April (Months) 2021 (Years)

  
**JESUS G. CATIGHUD**  
 Name and Signature of Employee


It is hereby certified that the above personnel can be assigned to this project, if the contract is awarded to our company.

**Borongan City – October 28, 2021**  
 (Place and Date)


  
**DONALDITO P. GASPAY**  
 The Authorized Representative

" Certified True Machine  
 Copy from the Original  


CONSTRUCTION FOREMAN


**REPUBLIC OF THE PHILIPPINES**  
 Philippine Postal Corporation  
**POSTAL IDENTITY CARD**

**FHLPOST**




Post Name: Actual Name, Surname, Initial

**JESUS GACOSTA CATIGHUD**

ADDRESS  
 UNIT-C MANALAYSAY CMPD DAGOHOY ST.  
 BAHAYANG PAGASA MOLINO III 4102  
 BACOR CITY CAVITE

<small>Date of Birth</small>	<small>Nationality</small>
27 Dec 68	PHL
<small>Issuing Post Office</small>	<small>Valid Until</small>
CAV-BC	01 Apr 22





PRN D49190155802-P

*Jesus Catighud*  
HOLDER'S SIGNATURE

*Joel L. Otarra*  
Postmaster General & CEO

**PREMIUM**


**REPUBLIC OF THE PHILIPPINES**  
 Province of Cavite  
 City of Bacoor  
**BARANGAY MOLINO III**  
 Tel. Nos. (049) 477-1888



ID NO. 19-93-3025


**LAST NAME FIRST NAME MIDDLE NAME**  
**CATIGHUD, JESUS GACOSTA**

**ADDRESS (No., Street, Subdivision, Barangay, City, Province)**  
 DAGOHOY ST. MANALAYSAY COMPOUND, MOLINO 3 CITY OF BACOR, CAVITE

<b>Birth Date</b>	<b>Status</b>	<b>Sex</b>	<b>Blood Type</b>	<b>Wt. (lbs.)</b>	<b>Ht. (ft.)</b>
12/27/1968	S	M	O	48kgs	5'4

**In case of emergency, please notify:**

**JESUS G. CATIGHUD**  
 DAGOHOY ST. MANALAYSAY COMPOUND, MOLINO 3 CITY OF BACOR, CAVITE  
 0919-2515728



Expires: 03/28/2021

*Jesus G. Catighud*  
**Signature**  
**Permanent**

" Certified True Machine Copy from Original "
